

Daily Coordination Meeting



14:00 Sign In


Daily Coordination Meeting

General Topics:

- Proper weekend shutdown
- Proper supervision and pass down during holidays



UTILITY LEVEL MOD1

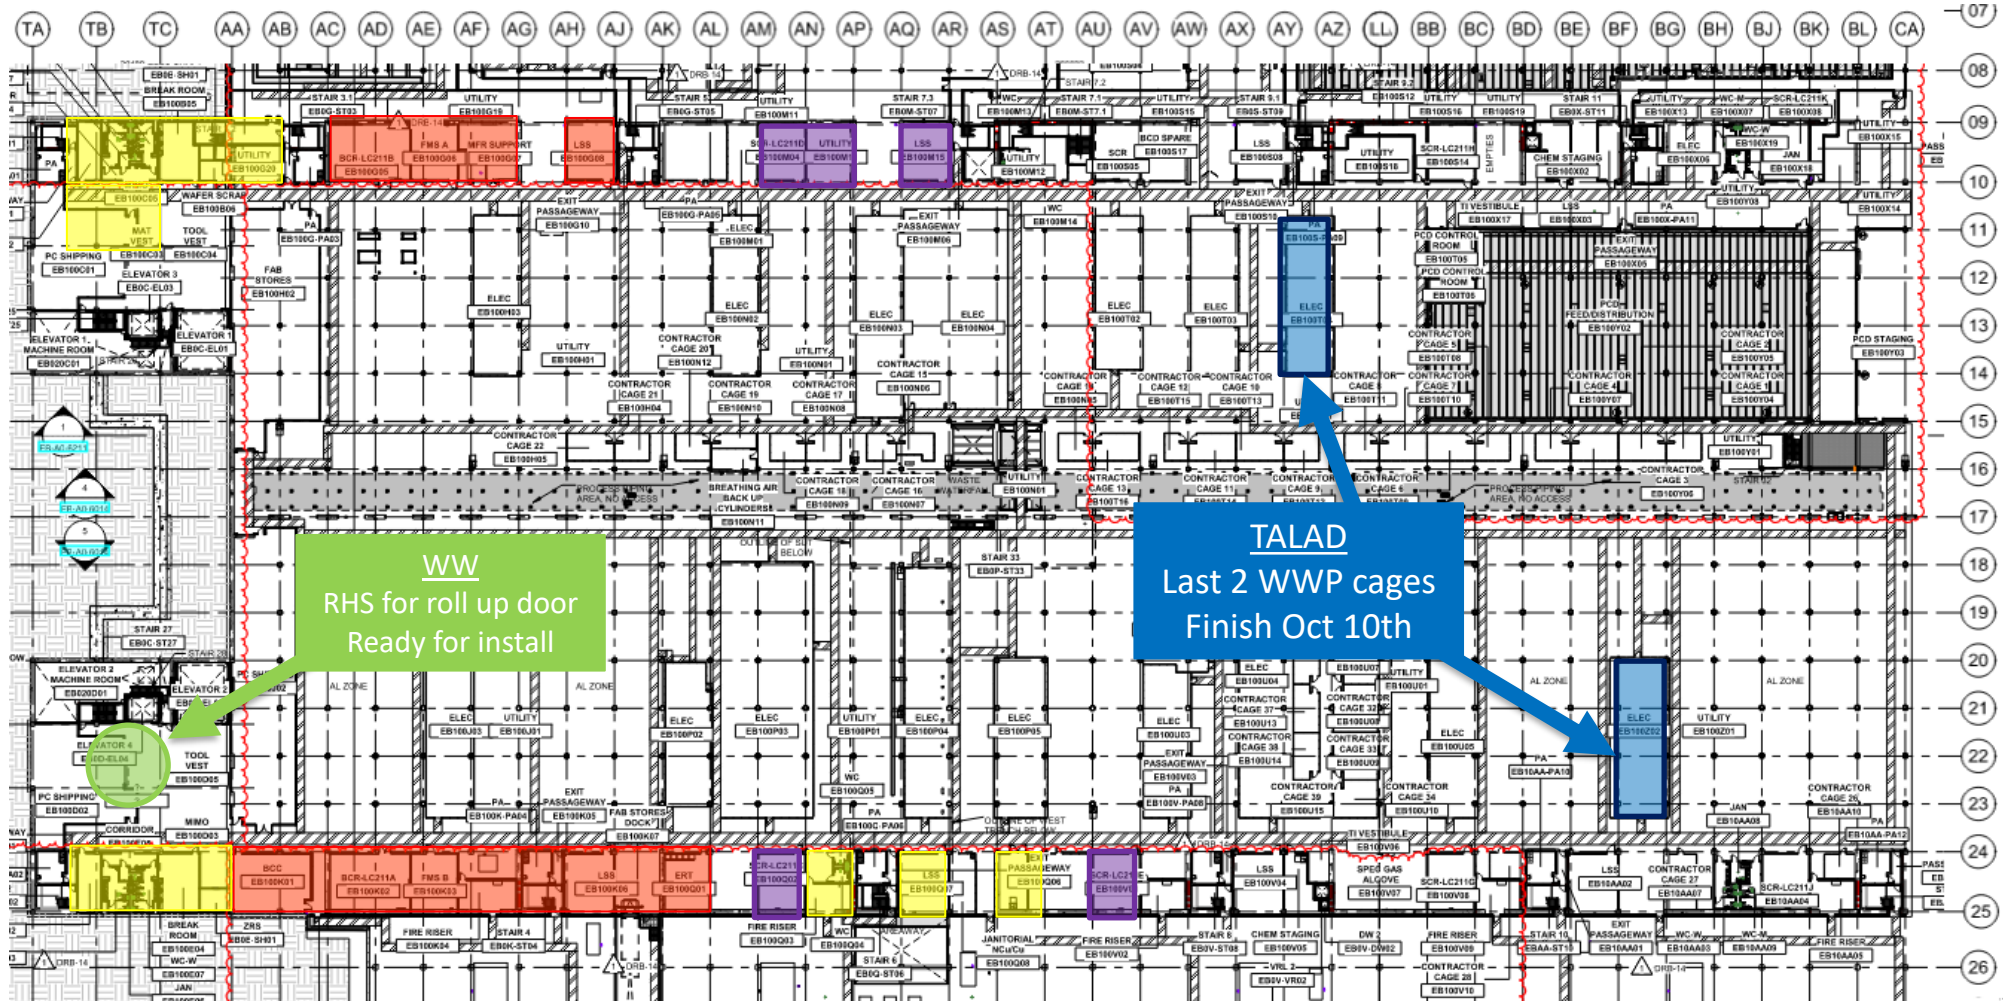

WW
RHS for roll up door
Ready for install

TALAD
Last 2 WWP cages
Finish Oct 10th

BELFOR
Mold remediation

ELRAM
Drywall install

MEP+Electrical
Ready for re-install



SUT 38.1 LEVEL


FROM SUNDAY

10/13


No access to
SUT1 at
east areaway

NO Access
Throw Stairs 29


Access
Throw Stairs 7.1
and Stairs 33

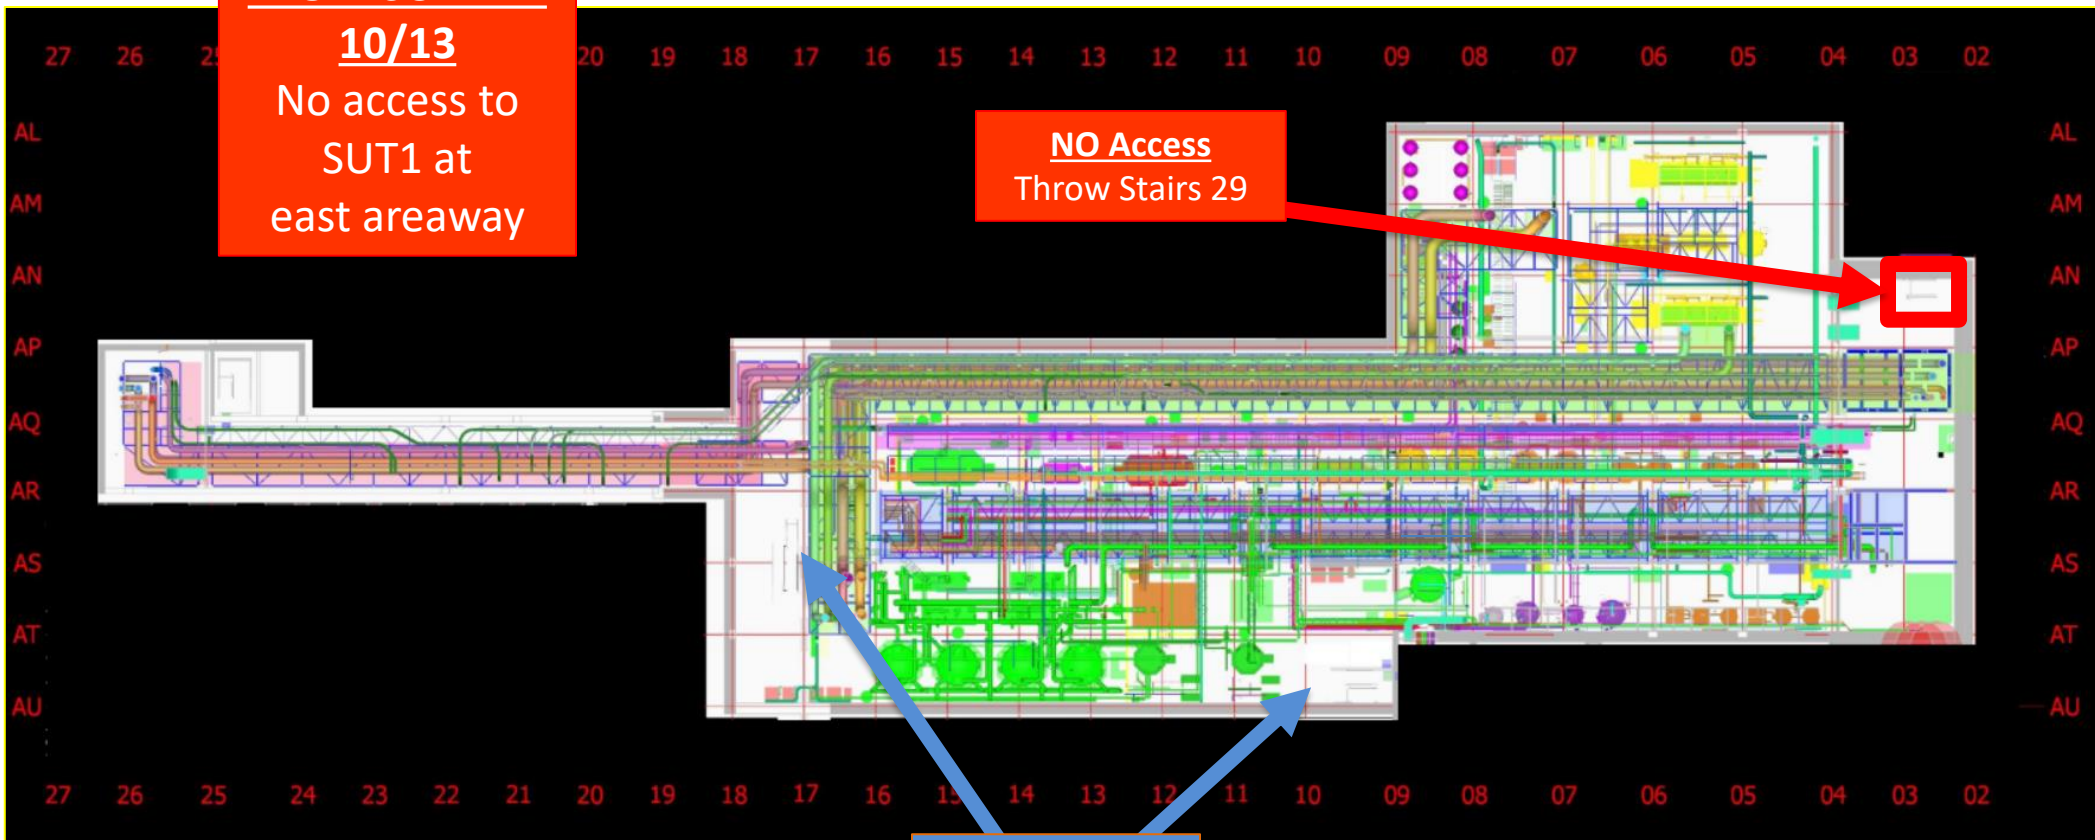

SUBFAB BUILDOUT MOD 1

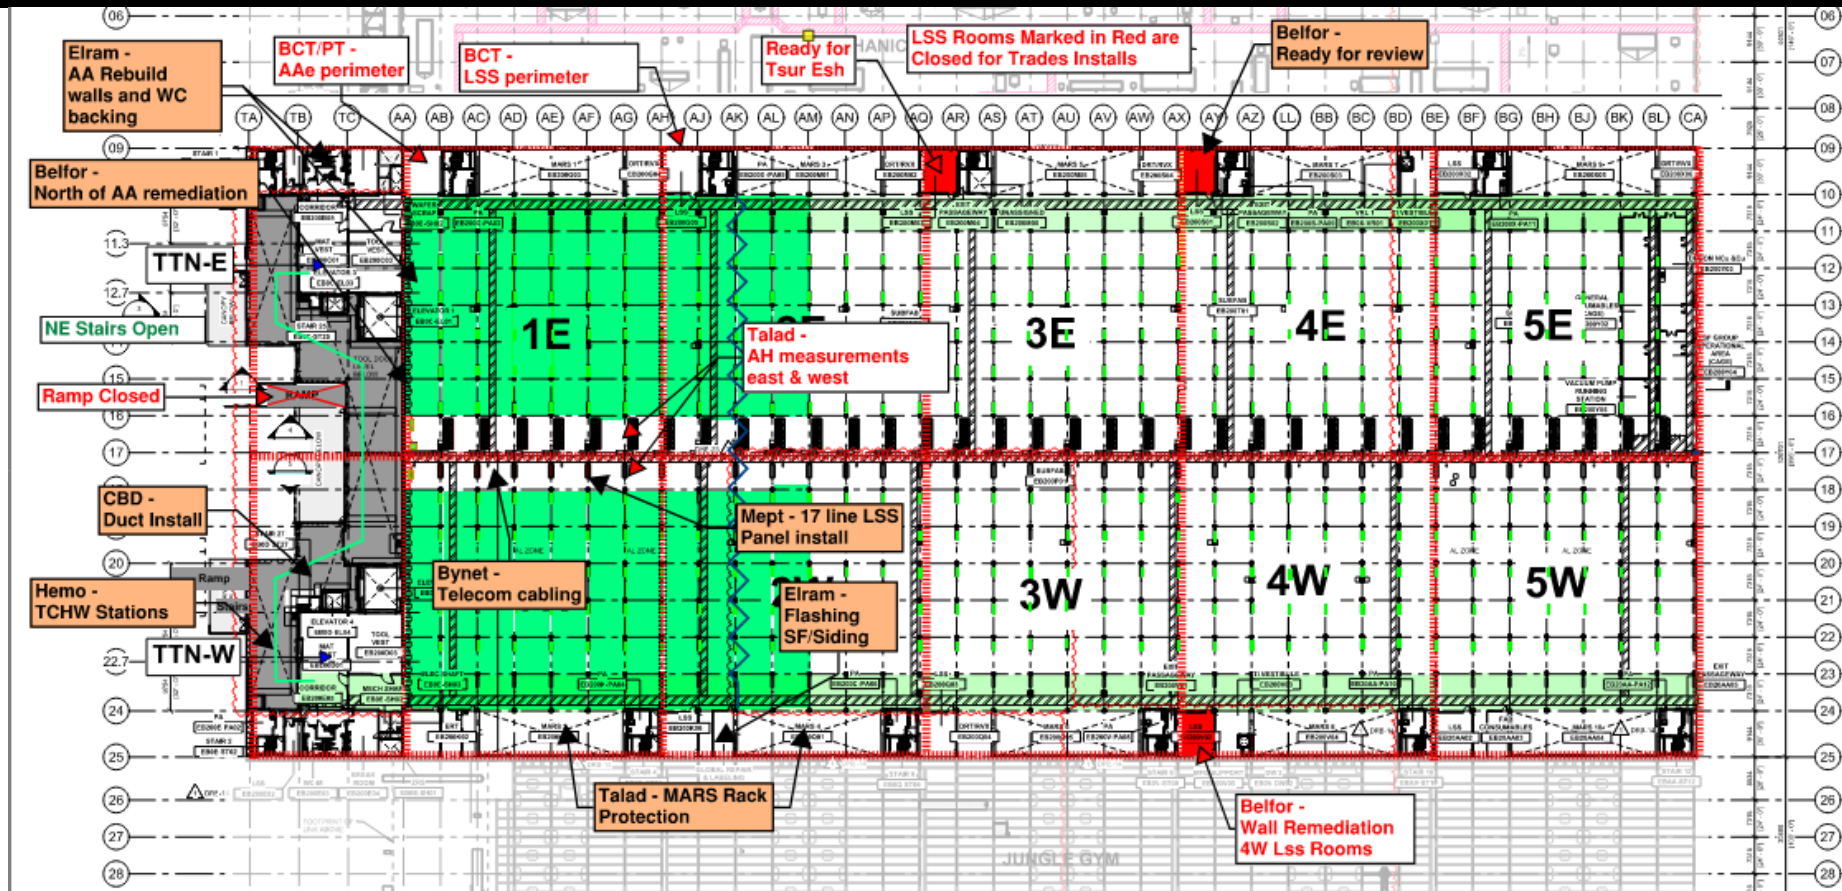


SUBFAB NWTT DELIVERIES BLOCKED

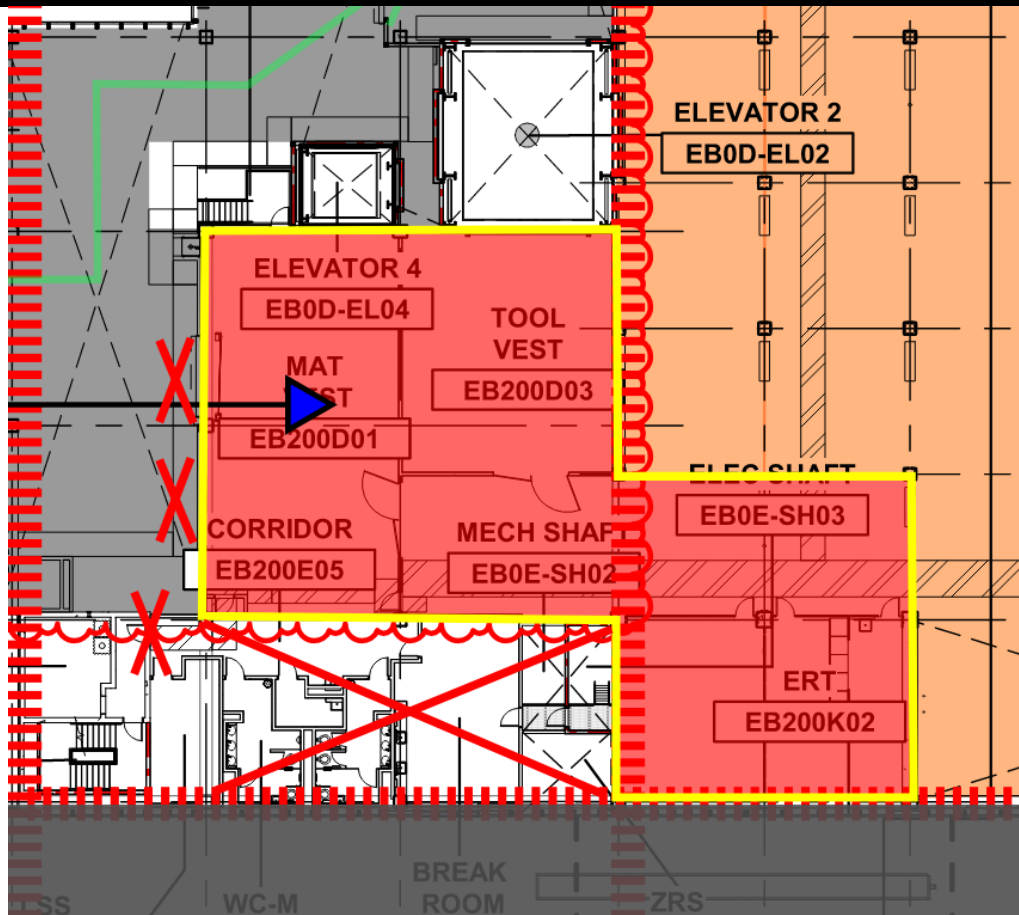


Northwest delivery dock is permanently closed.

Deliveries from MIMO7, MIMO9 & Alimak only.


SUBFAB CRC TOPCOAT

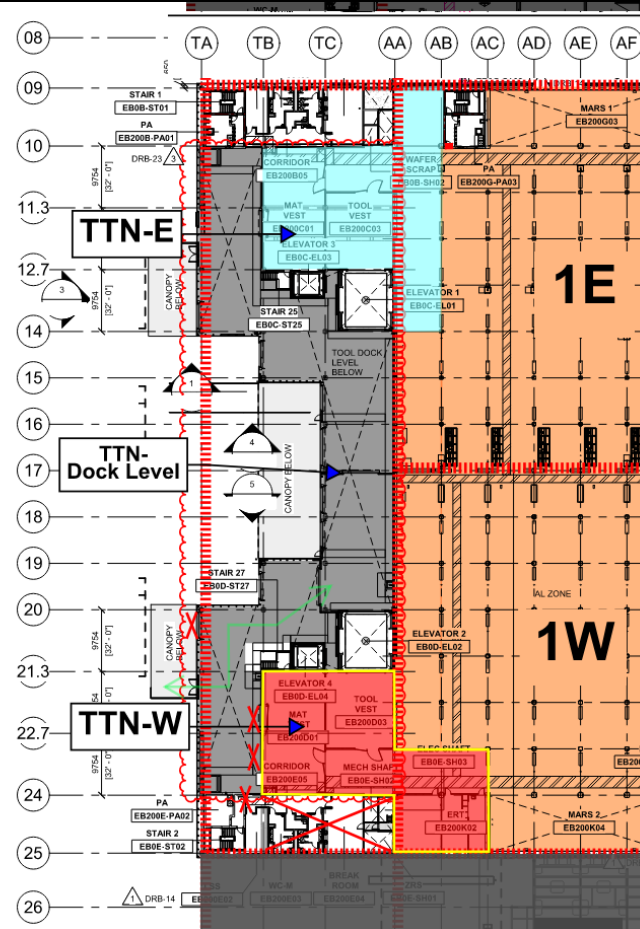

BCT Pressure Test Exclusion Zone

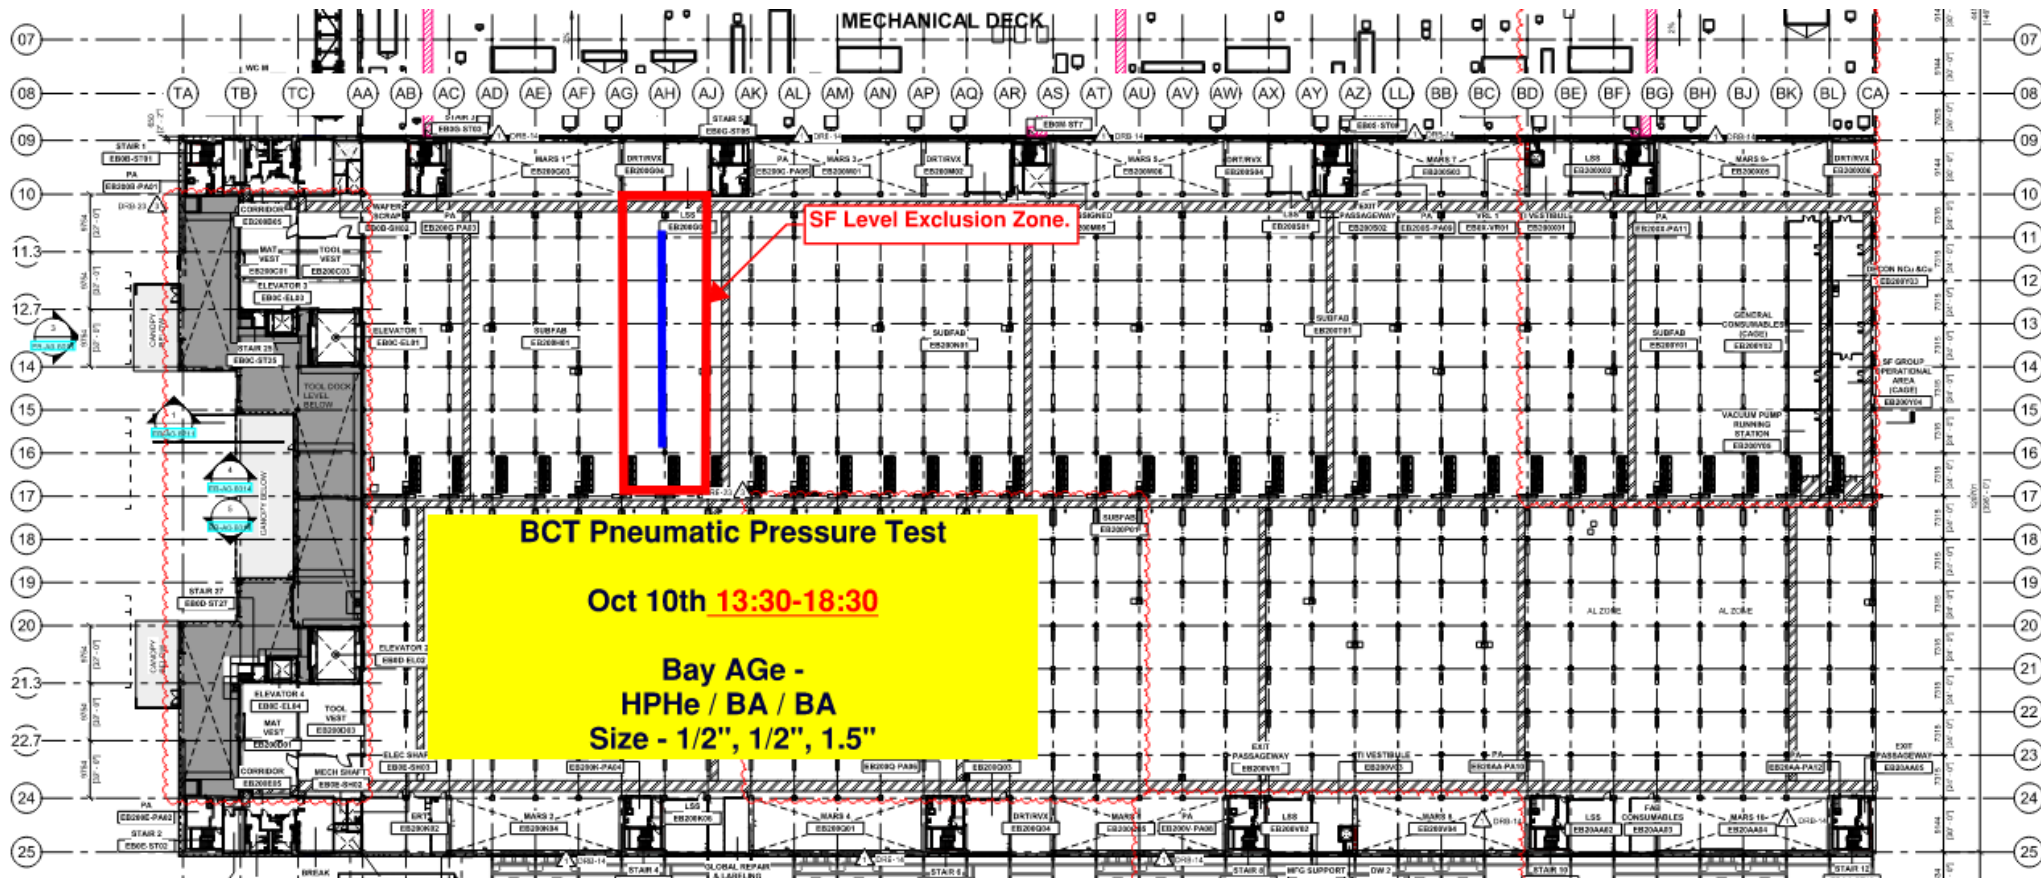

SUBFAB BUILDOUT MOD 2

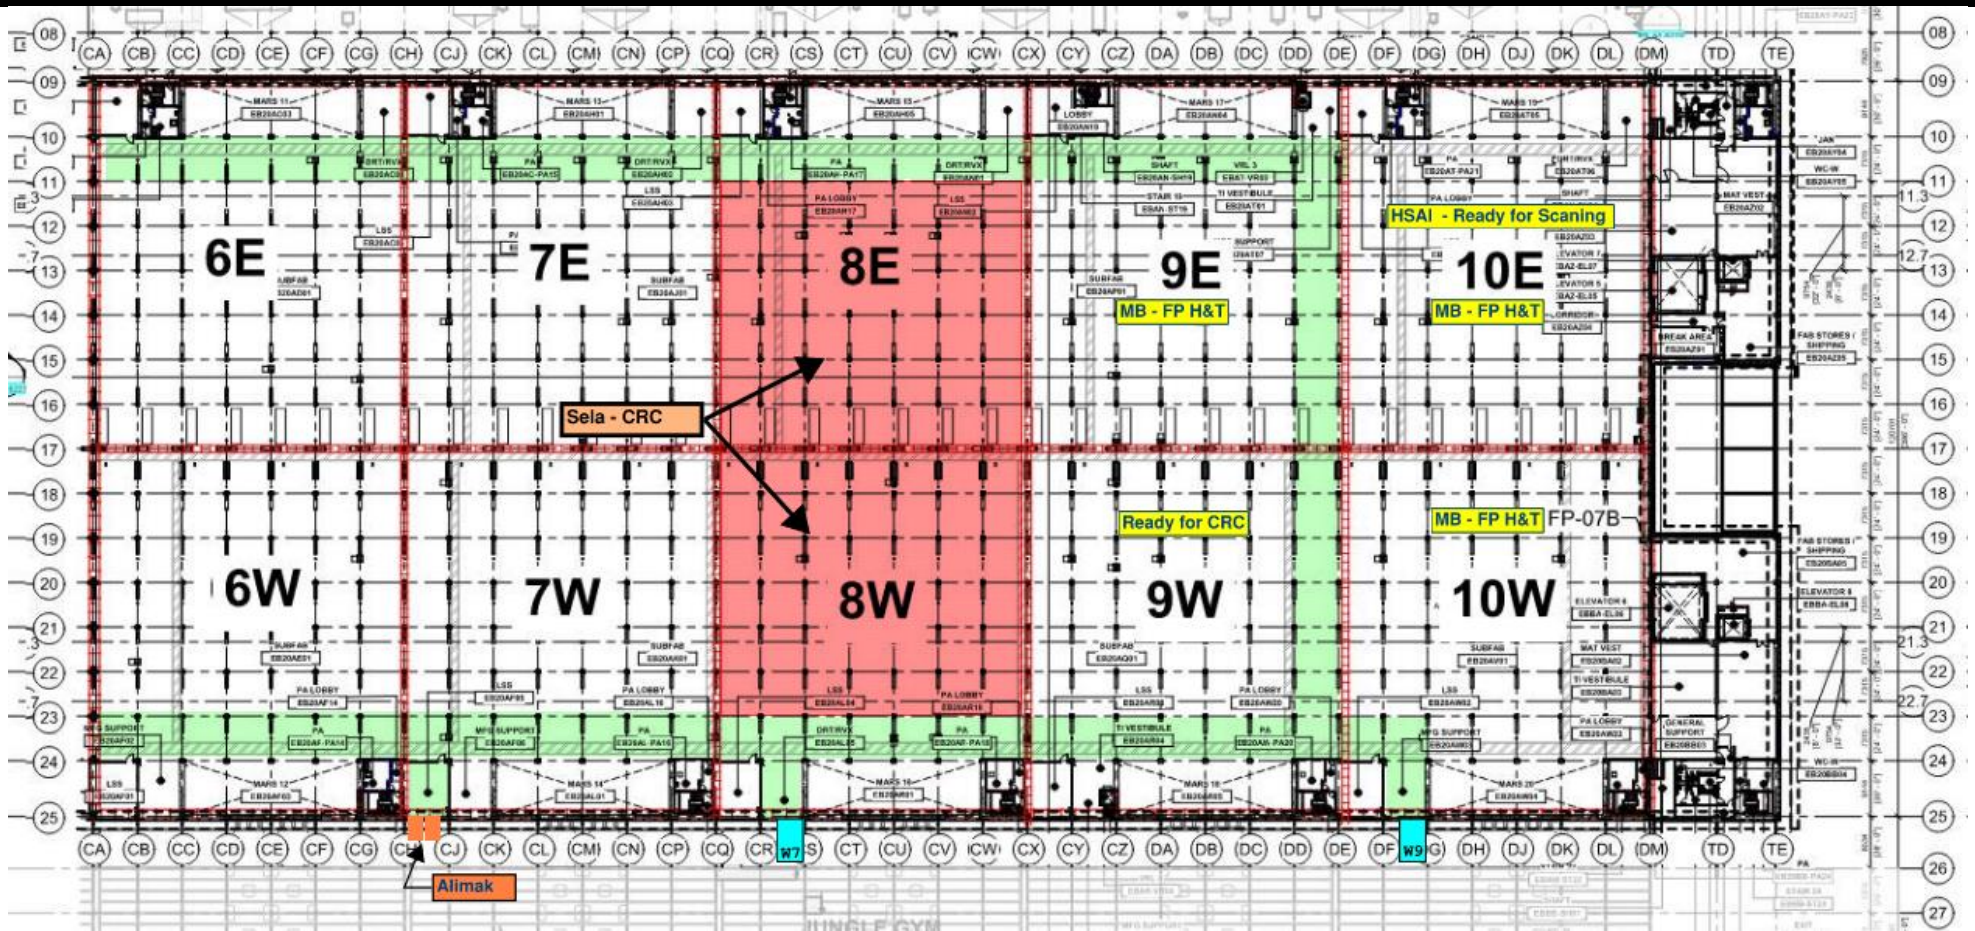


Clean room

protocols apply!!

1. only electrical booms & scissors.
2. Booties for all wheels is a must.

sella crc 1E zone.

All subs working over head must protect 4da working areas with protective sheets to prevent plaster waste or any other waste from falling down on fresh crc coat

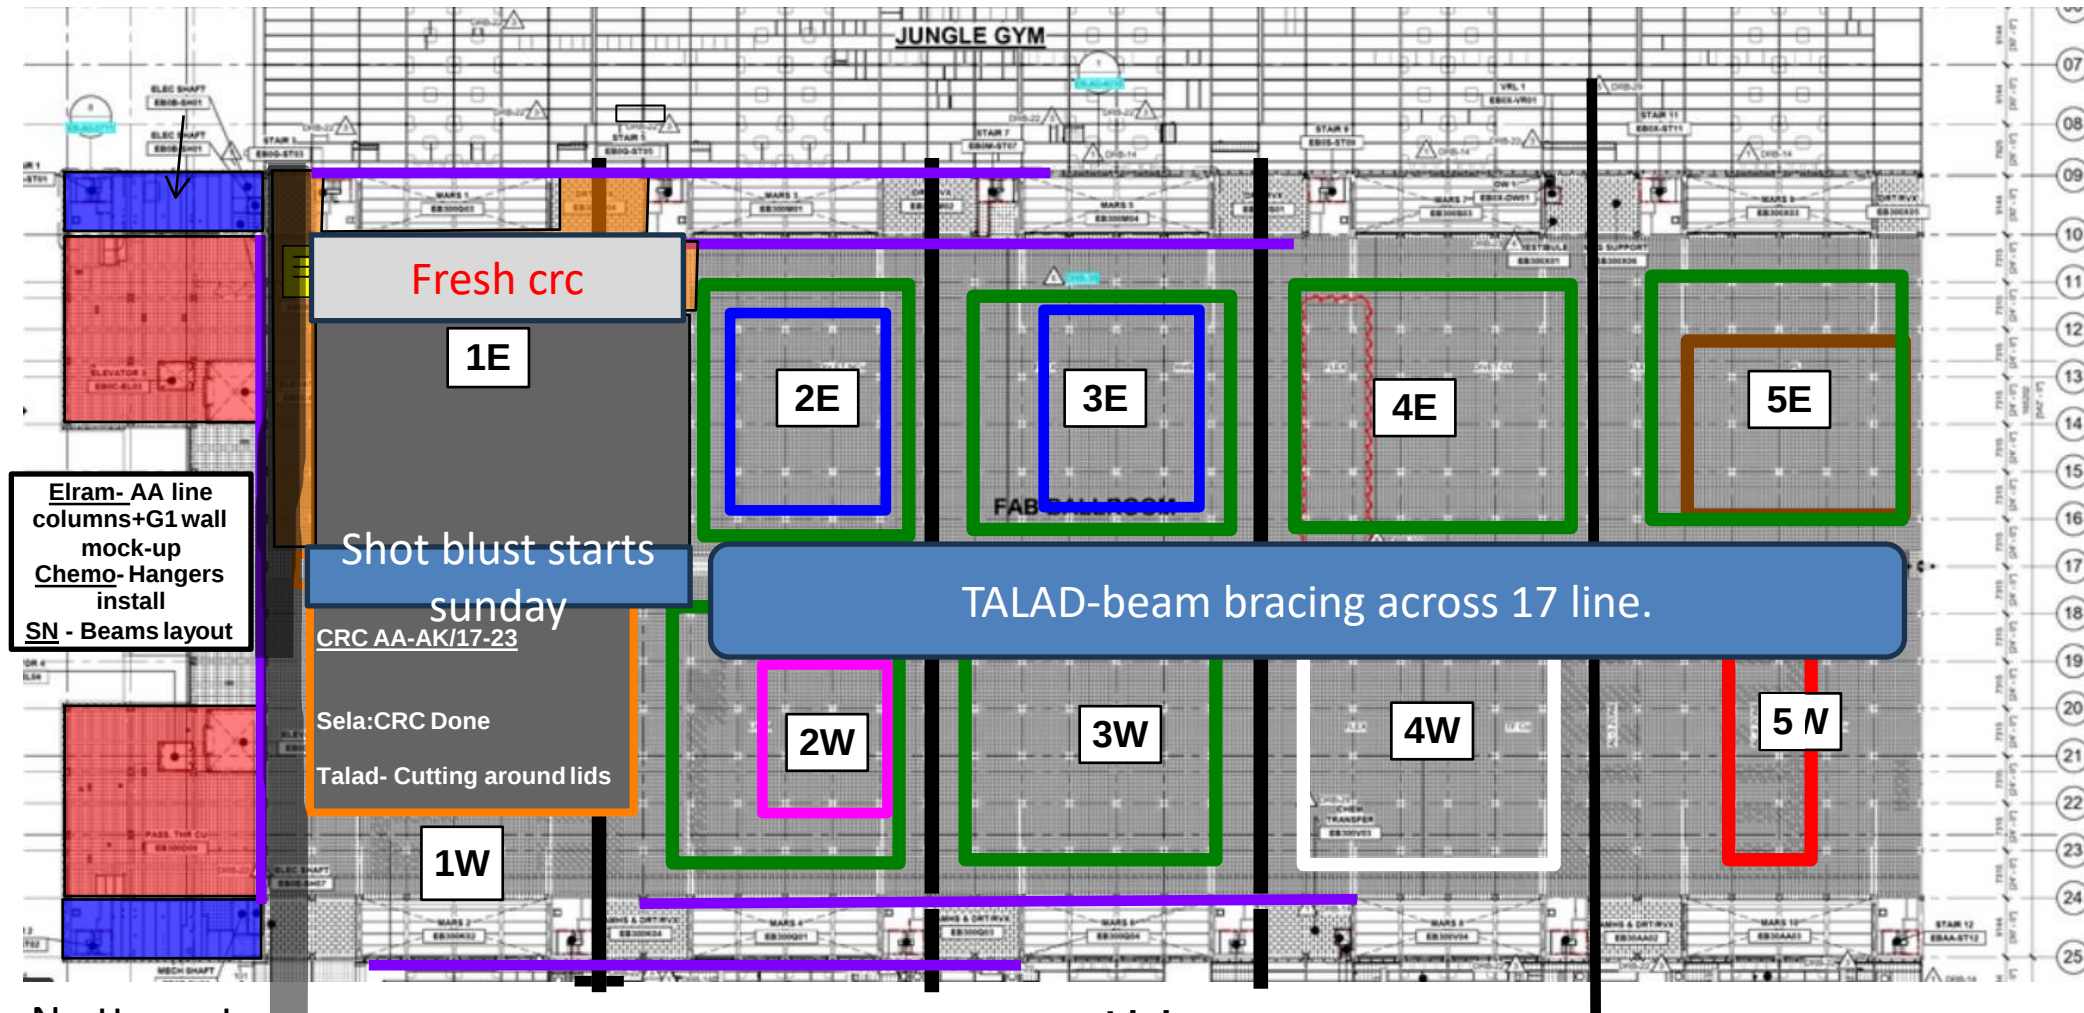

Nwtt must be clear for paint.

BLOWDOWN WALL IS COMING NEXT WEEK.



Link

SIG - Mobile scaffold installment

Afcon- Rack install.


Newcotech-BLOWDOWN TEMP WALL

Pach-taas - exsfm135 duct installment

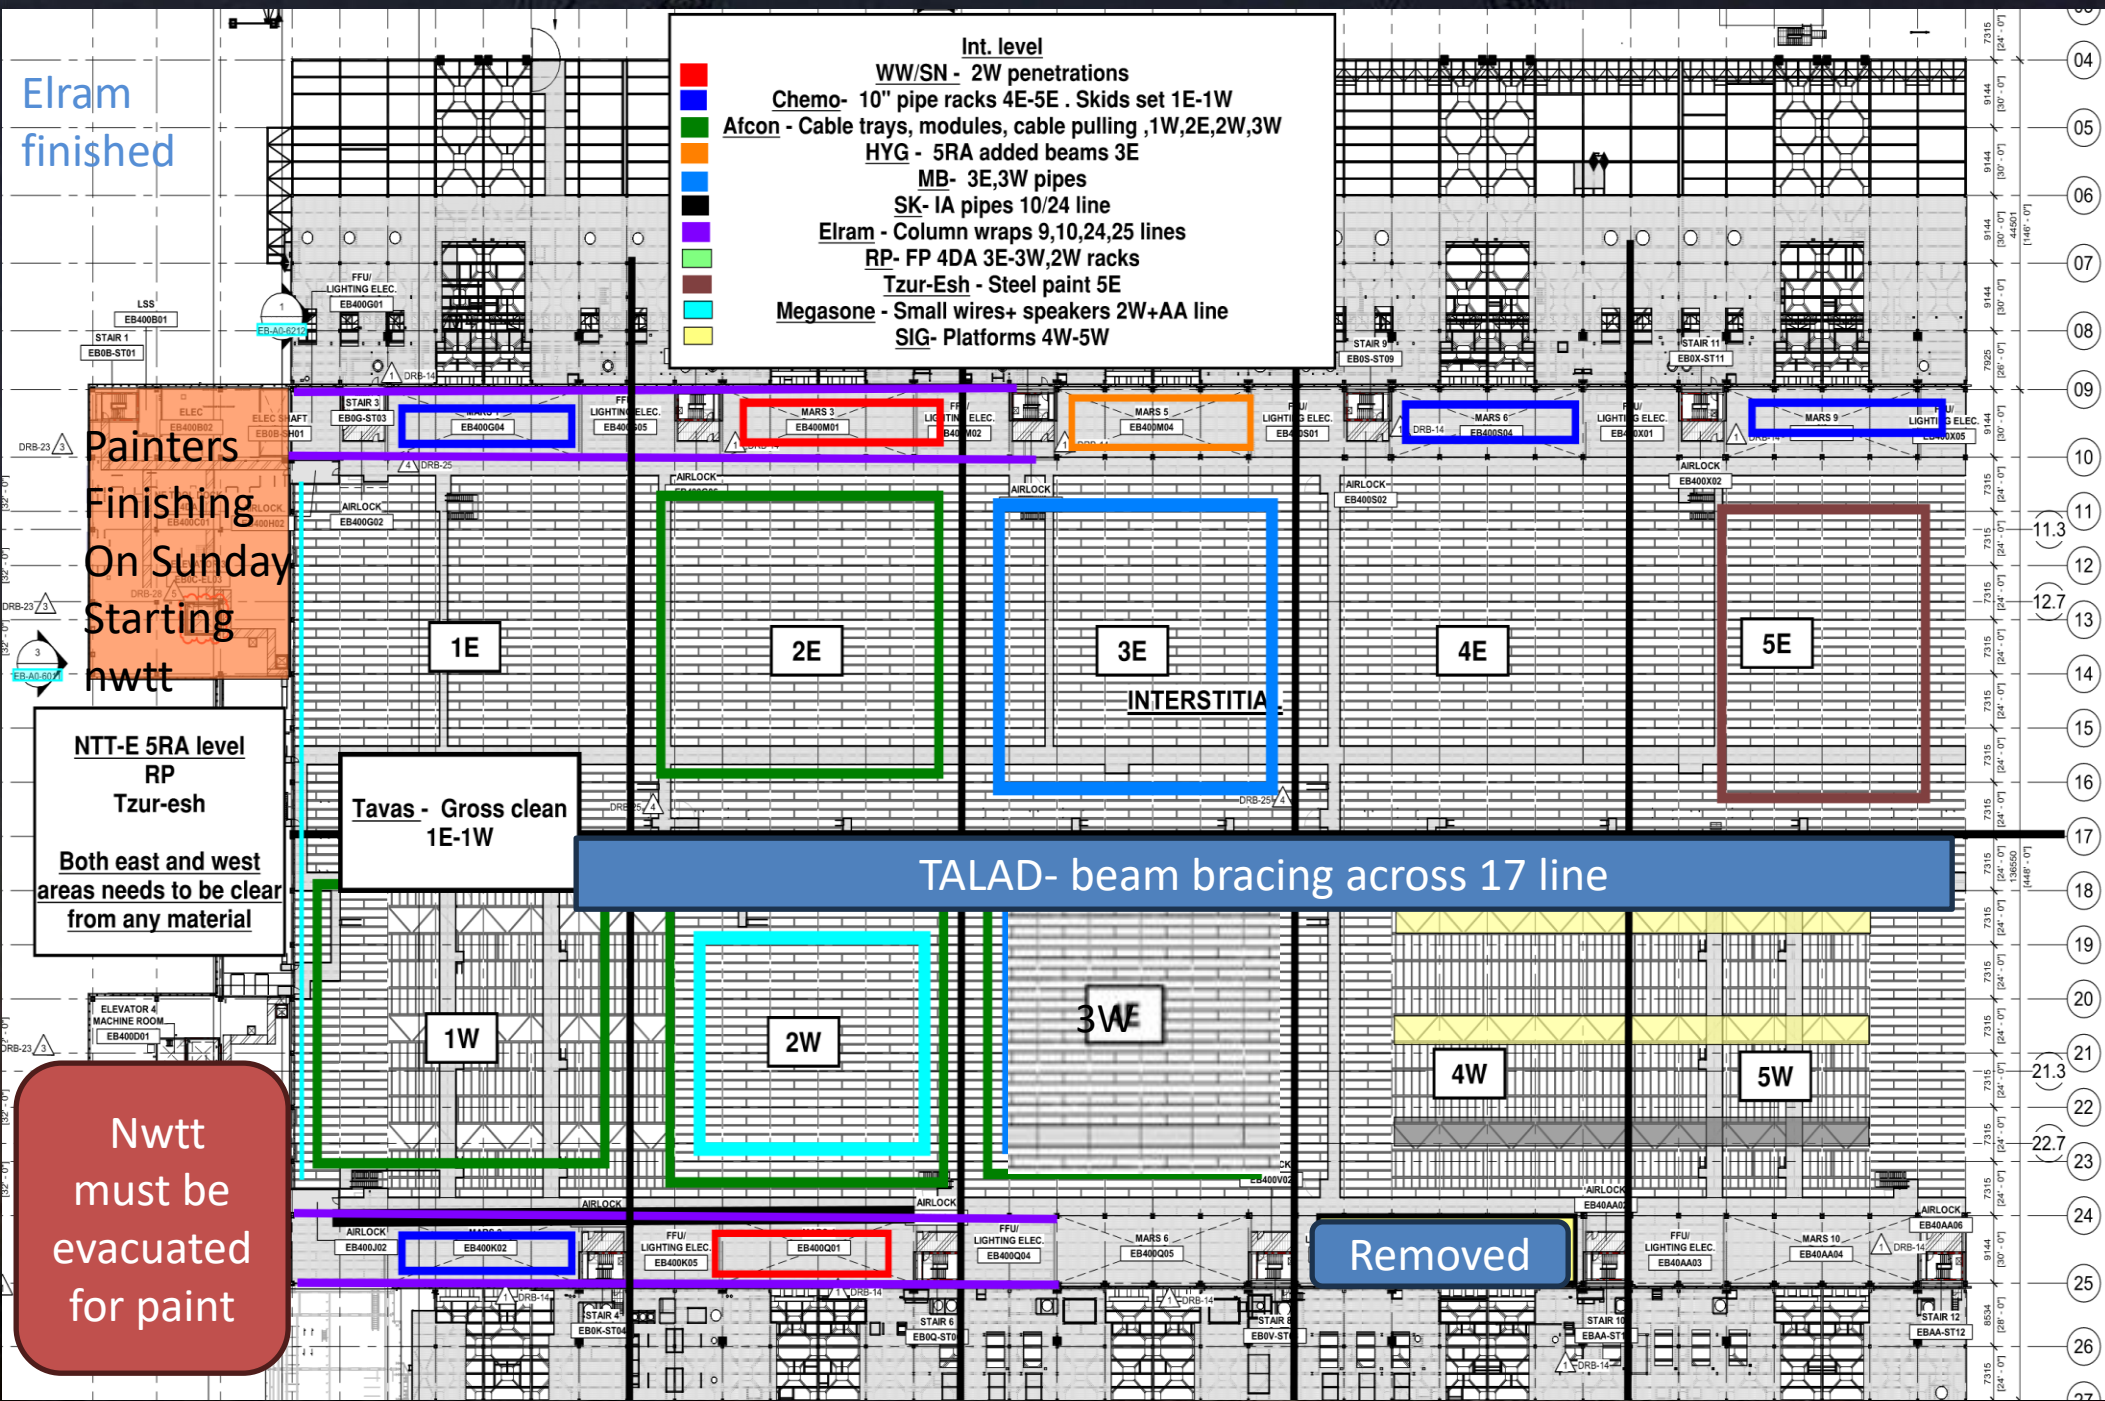





Clean Room Wall Of Shame

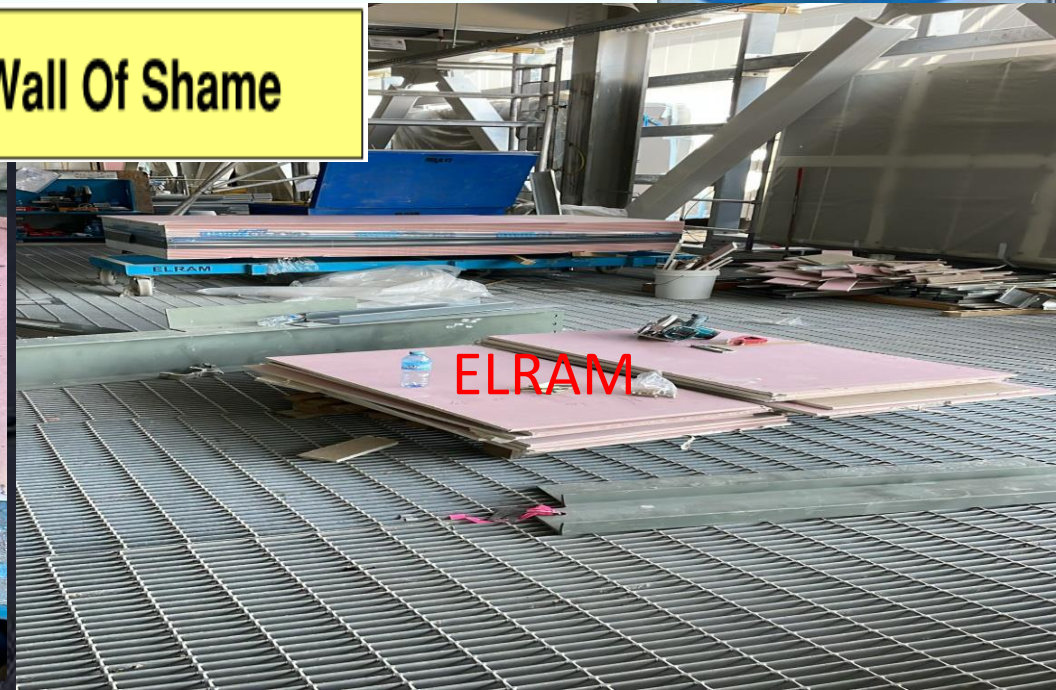



MALCHIMIM BADAROM


Safety violation
over loaded frp.

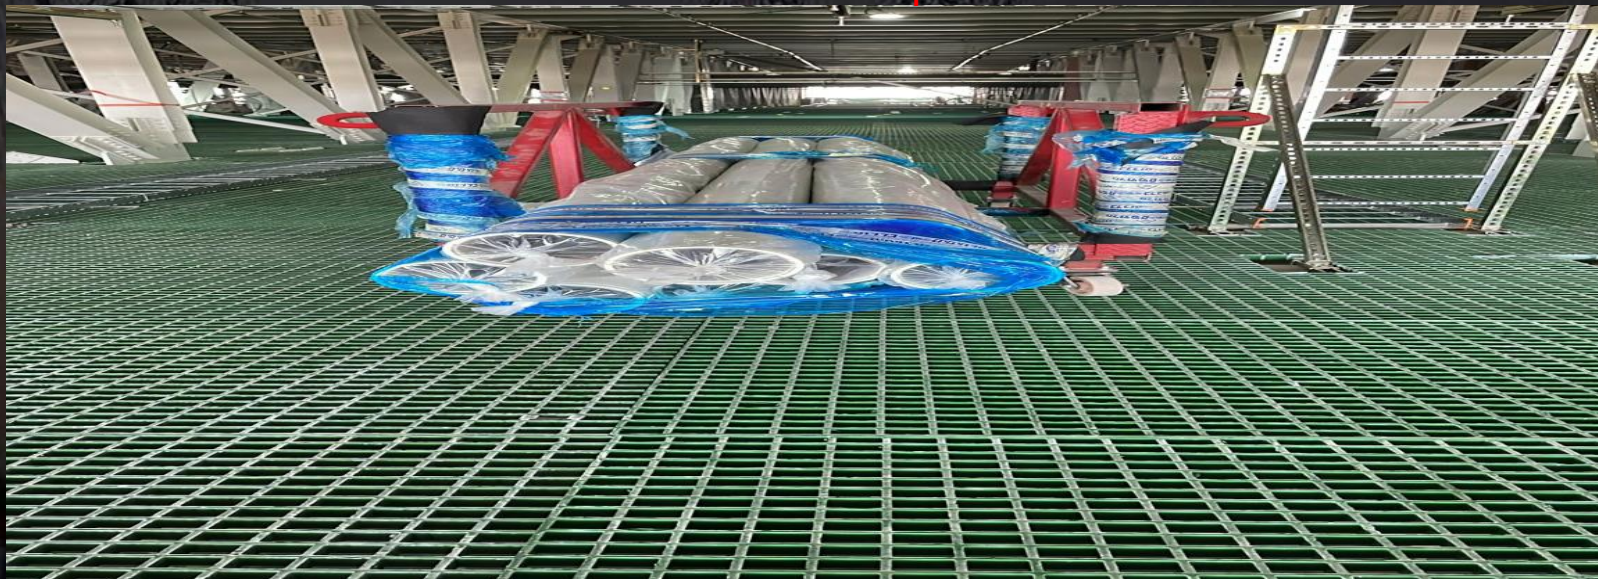

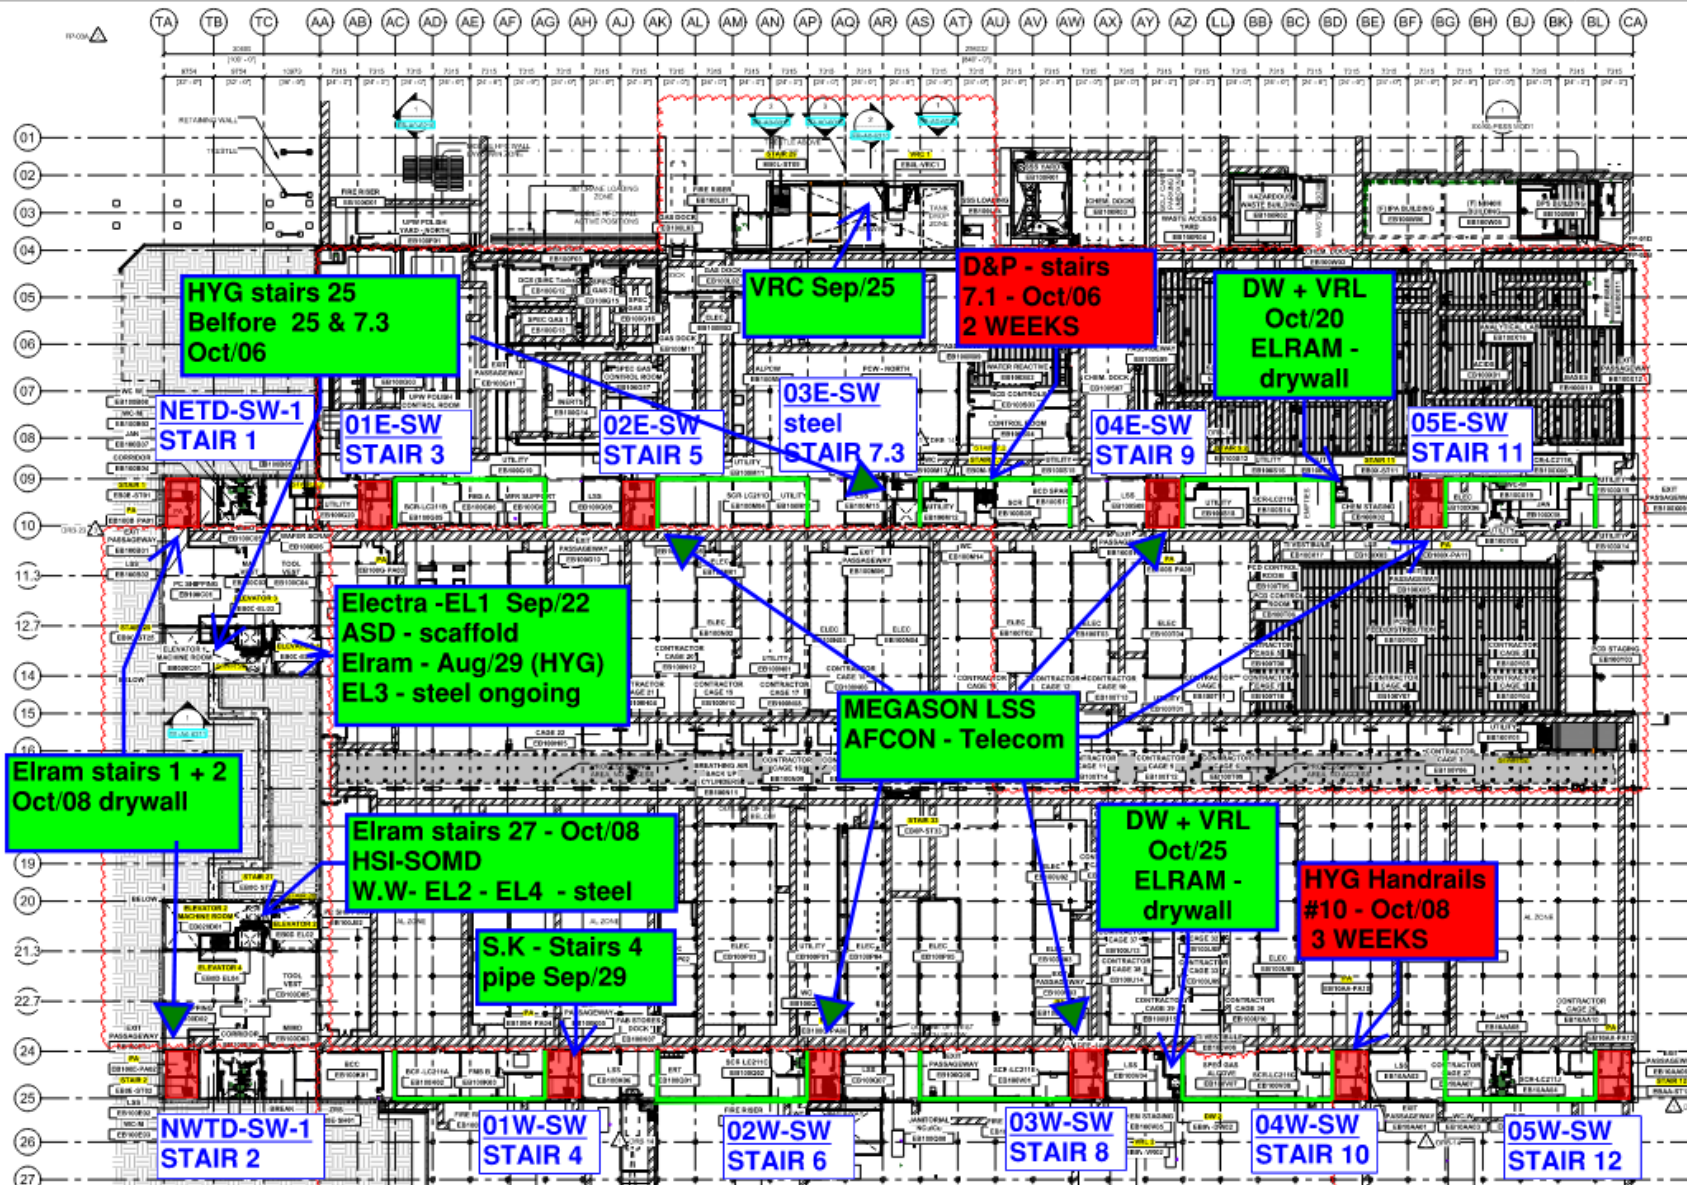

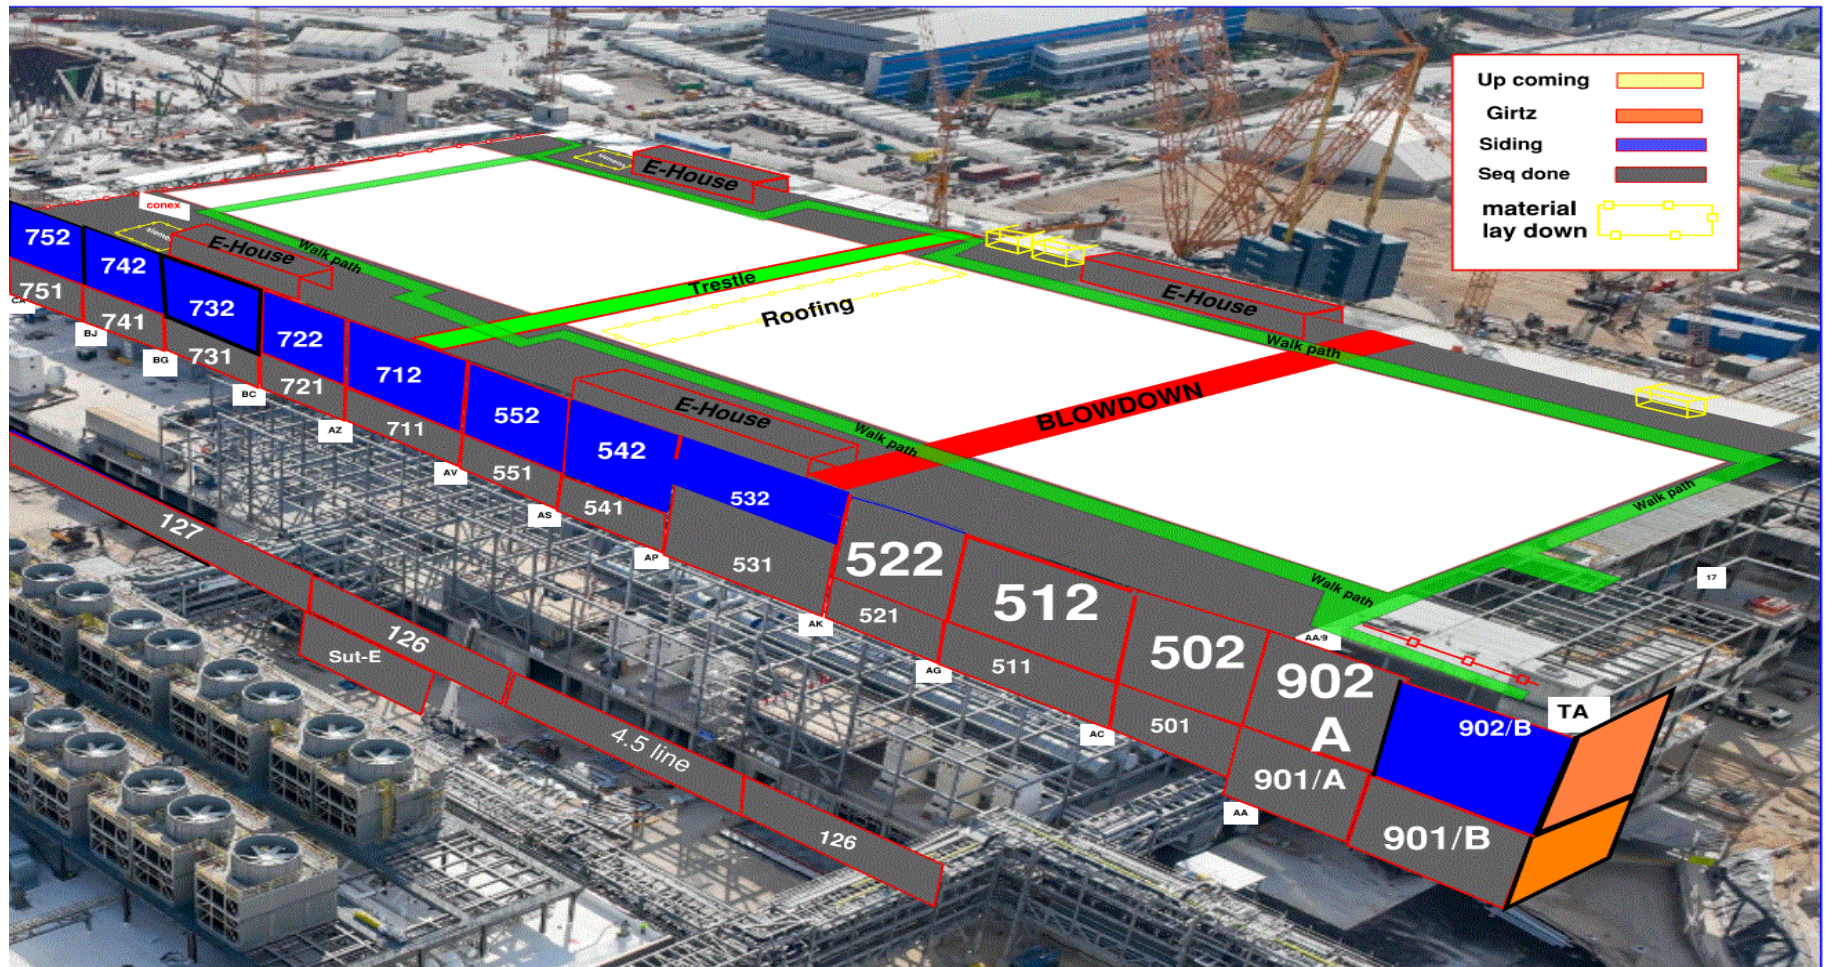

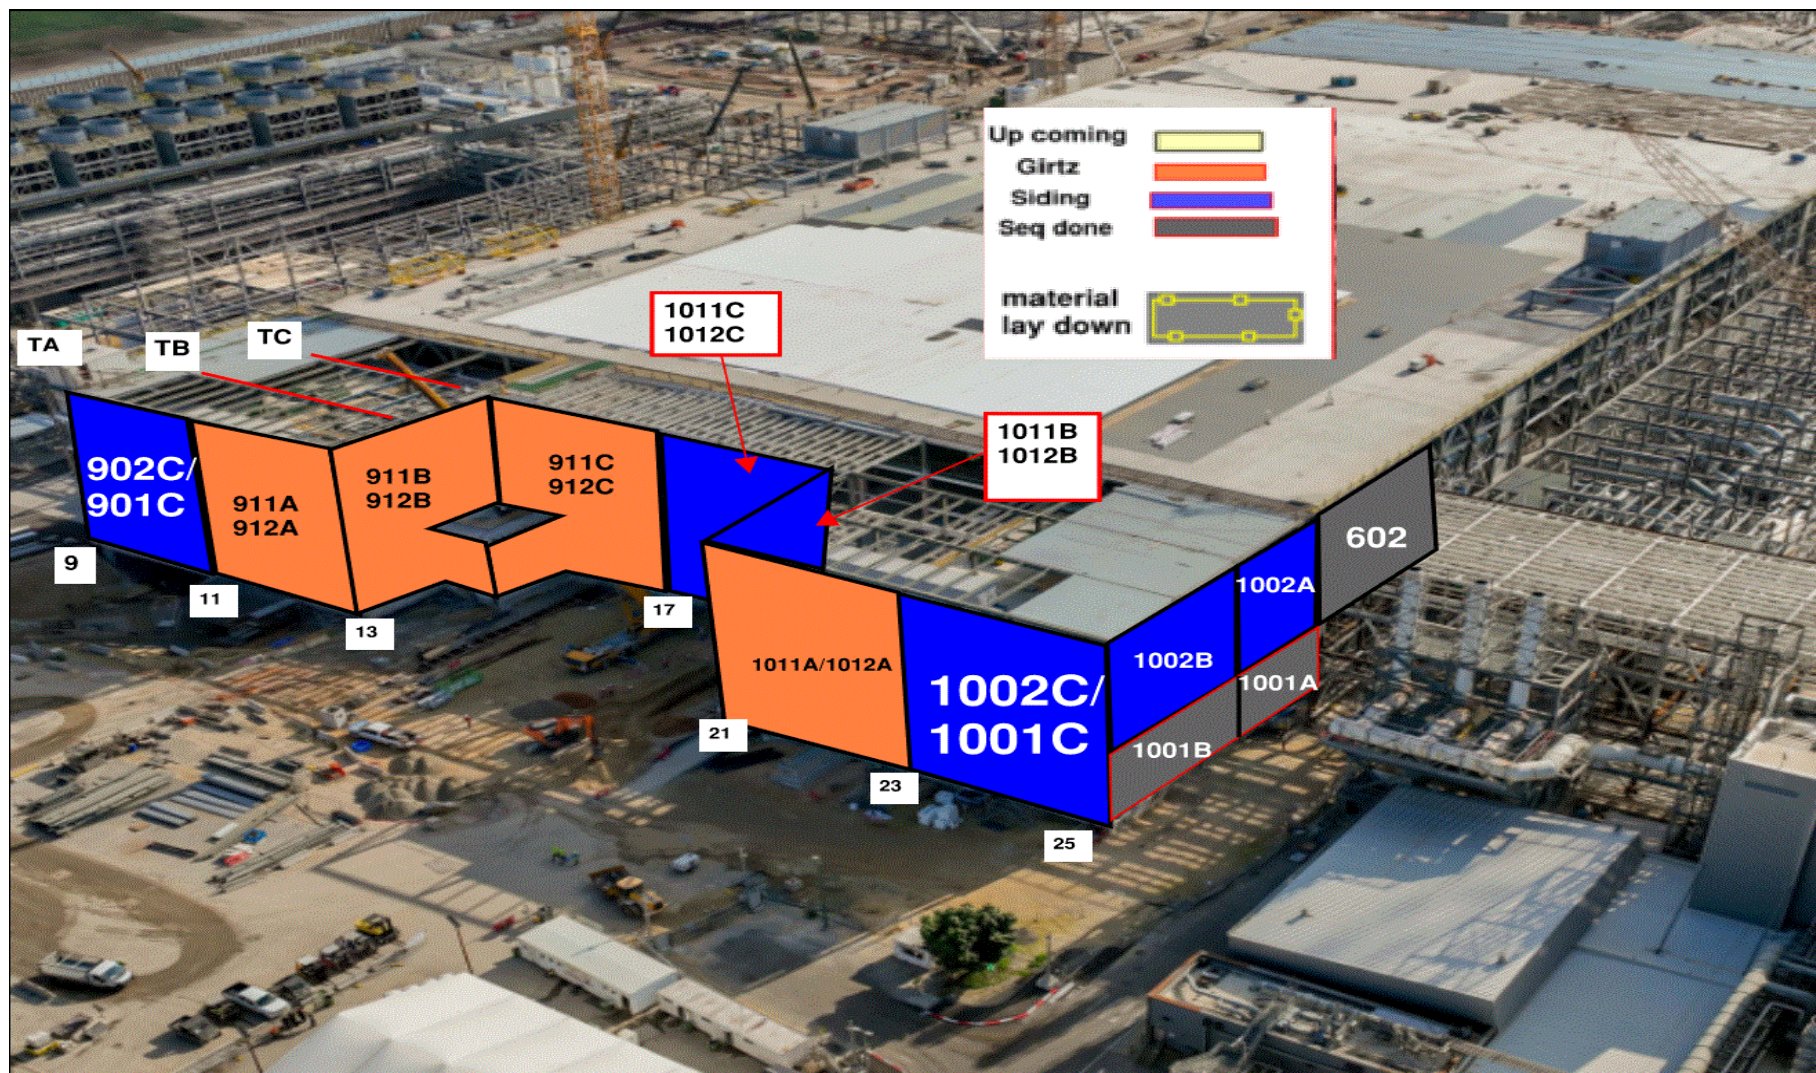

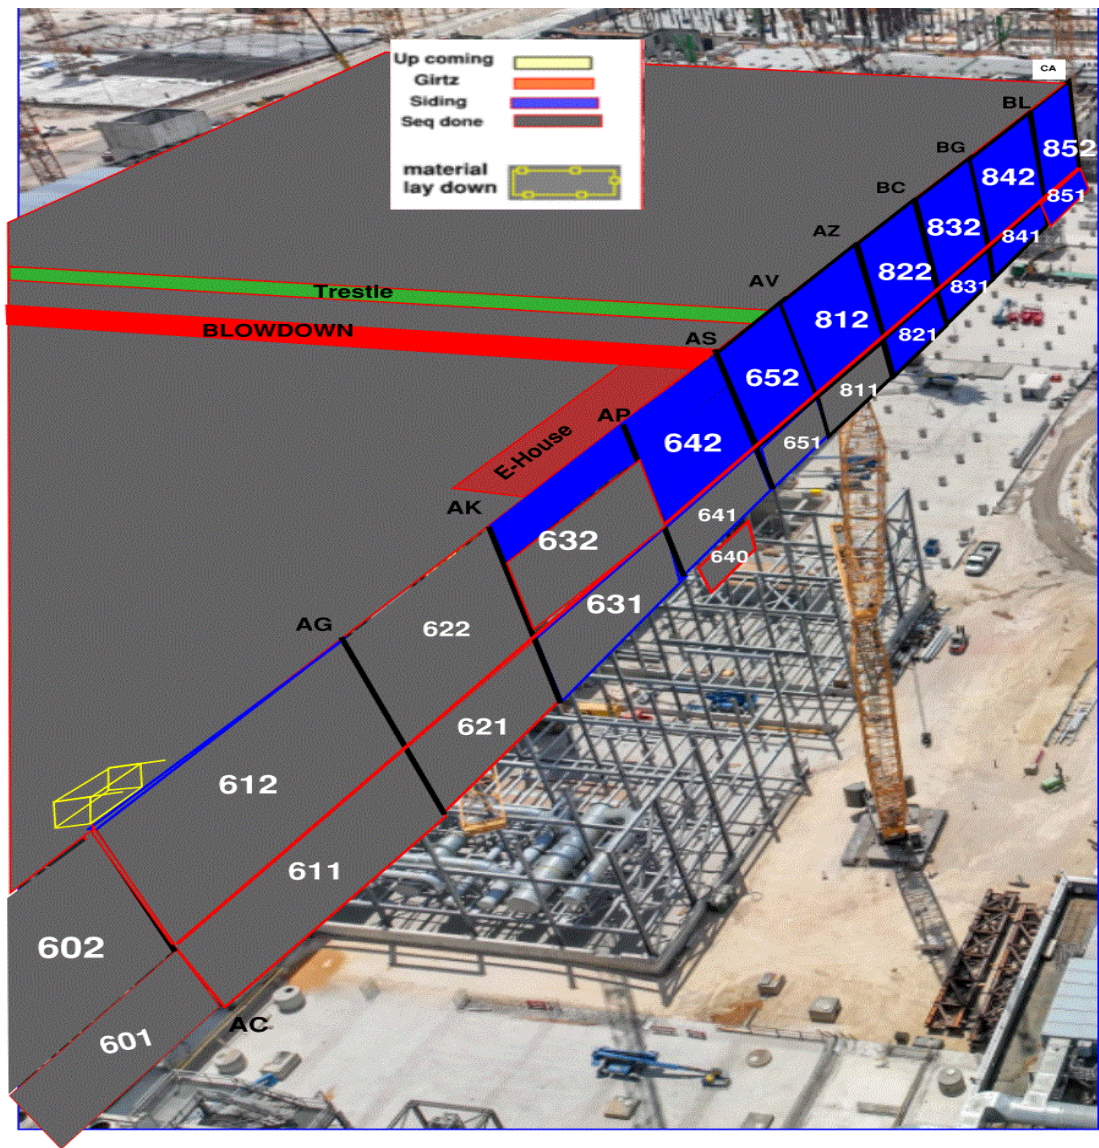

Siding - East FAB - PSSS

BLOWDOWN 30%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
CA	CB	CC	CD	CE	CF	CG	CH	CI	CJ	CK	CL	CM	CN	CO	CP	CQ	CR	CS	CT	CU	CV	CW	CX	CY	CZ	DA	DB	DC	DD	DE	DF	DG	DH	DI	DJ	DK	DL	DM	DN	DO	DP	DQ	DR	DS	DT	DU	DV	DW	DX	DY	DZ	EA	EB	EC	ED	EE	EF	EG	EH	EI	EJ	EK	EL	EM	EN	EO	EP	EQ	ER	ES	ET	EU	EV	EW	EX	EY	EZ	FA	FB	FC	FD	FE	FF	FG	FH	FI	FJ	FK	FL	FM	FN	FO	FP	FQ	FR	FS	FT	FU	FV	FW	FX	FY	FZ	GA	GB	GC	GD	GE	GF	GG	GH	GI	GJ	GK	GL	GM	GN	GO	GP	GQ	GR	GS	GT	GU	GV	GW	GX	GY	GZ	HA	HB	HC	HD	HE	HF	HG	HH	HI	HJ	HK	HL	HM	HN	HO	HP	HQ	HR	HS	HT	HU	HV	HW	HX	HY	HZ	IA	IB	IC	ID	IE	IF	IG	IH	II	IJ	IK	IL	IM	IN	IO	IP	IQ	IR	IS	IT	IU	IV	IW	IX	IY	IZ	JA	JB	JC	JD	JE	JF	JG	JH	JI	JJ	JK	JL	JM	JN	JO	JP	JQ	JR	JS	JT	JU	JV	JW	JX	JY	JZ	KA	KB	KC	KD	KE	KF	KG	KH	KI	KJ	KK	KL	KM	KN	KO	KP	KQ	KR	KS	KT	KU	KV	KW	KX	KY	KZ	LA	LB	LC	LD	LE	LF	LG	LH	LI	LJ	LK	LL	LM	LN	LO	LP	LQ	LR	LS	LT	LU	LV	LW	LX	LY	LZ	MA	MB	MC	MD	ME	MF	MG	MH	MI	MJ	MK	ML	MM	MN	MO	MP	MQ	MR	MS	MT	MU	MV	MW	MX	MY	MZ	NA	NB	NC	ND	NE	NF	NG	NH	NI	NJ	NK	NL	NM	NN	NO	NP	NQ	NR	NS	NT	NU	NV	NW	NX	NY	NZ	OA	OB	OC	OD	OE	OF	OG	OH	OI	OJ	OK	OL	OM	ON	OO	OP	OQ	OR	OS	OT	OU	OV	OW	OX	OY	OZ	PA	PB	PC	PD	PE	PF	PG	PH	PI	PJ	PK	PL	PM	PN	PO	PP	PQ	PR	PS	PT	PU	PV	PW	PX	PY	PZ	QA	QB	QC	QD	QE	QF	QG	QH	QI	QJ	QK	QL	QM	QN	QO	QP	QQ	QR	QS	QT	QU	QV	QW	QX	QY	QZ	RA	RB	RC	RD	RE	RF	RG	RH	RI	RJ	RK	RL	RM	RN	RO	RP	RQ	RR	RS	RT	RU	RV	RW	RX	RY	RZ	SA	SB	SC	SD	SE	SF	SG	SH	SI	SJ	SK	SL	SM	SN	SO	SP	SQ	SR	SS	ST	SU	SV	SW	SX	SY	SZ	TA	TB	TC	TD	TE	TF	TG	TH	TI	TJ	TK	TL	TM	TN	TO	TP	TQ	TR	TS	TT	TU	TV	TW	TX	TY	TZ	UA	UB	UC	UD	UE	UF	UG	UH	UI	UJ	UK	UL	UM	UN	UO	UP	UQ	UR	US	UT	UU	UV	UW	UX	UY	UZ	VA	VB	VC	VD	VE	VF	VG	VH	VI	VJ	VK	VL	VM	VN	VO	VP	VQ	VR	VS	VT	VU	VV	VW	VX	VY	VZ	WA	WB	WC	WD	WE	WF	WG	WH	WI	WJ	WK	WL	WM	WN	WO	WP	WQ	WR	WS	WT	WU	WV	WW	WX	WY	WZ	XA	XB	XC	XD	XE	XF	XG	XH	XI	XJ	XK	XL	XM	XN	XO	XP	XQ	XR	XS	XT	XU	XV	XW	XX	XY	XZ	YA	YB	YC	YD	YE	YF	YG	YH	YI	YJ	YK	YL	YM	YN	YO	YP	YQ	YR	YS	YT	YU	YV	YW	YX	YY	YZ	ZA	ZB	ZC	ZD	ZE	ZF	ZG	ZH	ZI	ZJ	ZK	ZL	ZM	ZN	ZO	ZP	ZQ	ZR	ZS	ZT	ZU	ZV	ZW	ZX	ZY	ZZ
24	751 / 752	24	741 / 742	24	731 / 732	24	721 / 722	24	711 / 712	24	701 / 702	24	691 / 692	24	681 / 682	24	671 / 672	24	661 / 662	24	651 / 652	24	641 / 642	24	631 / 632	24	621 / 622	24	611 /																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		

Siding - West FAB - JYG


Link

1
2
3
4
5

PSSS.1

Utility Level 1YA


PSSS Roof 2SA

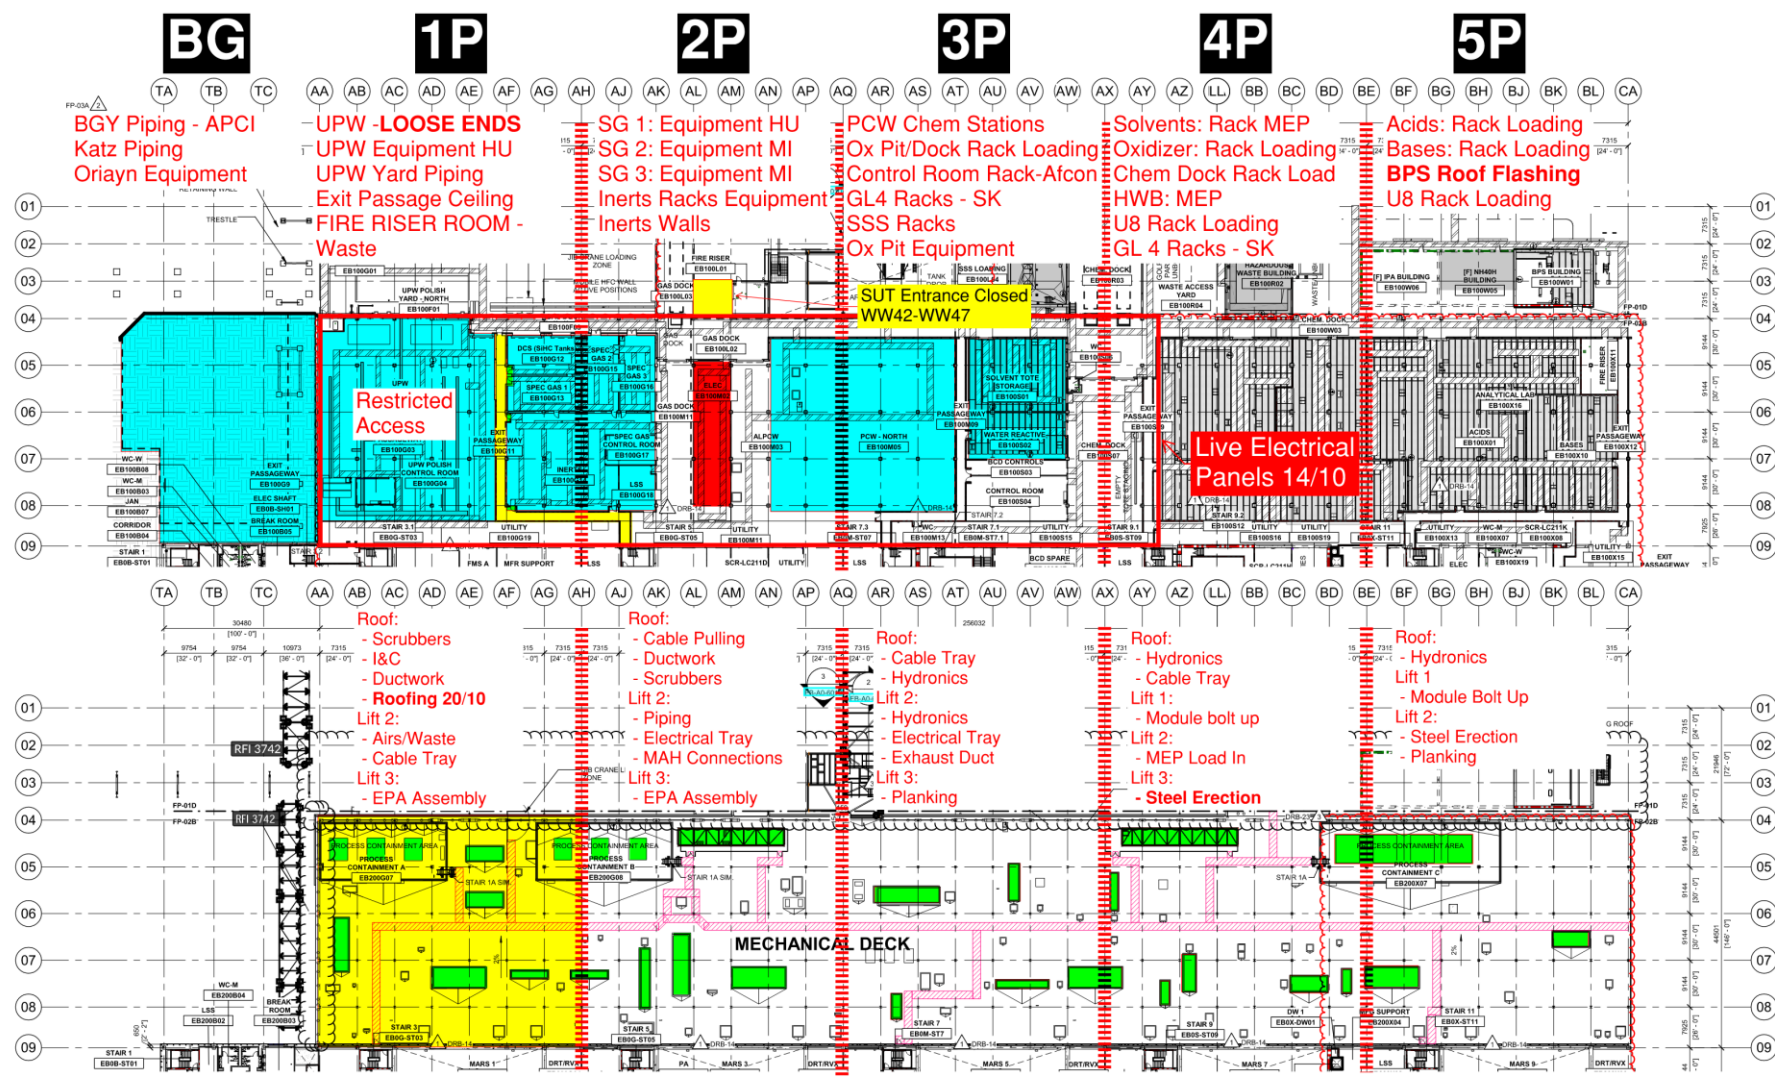


PSSS.2

Utility Level
1YA

PSSS Roof
2SA

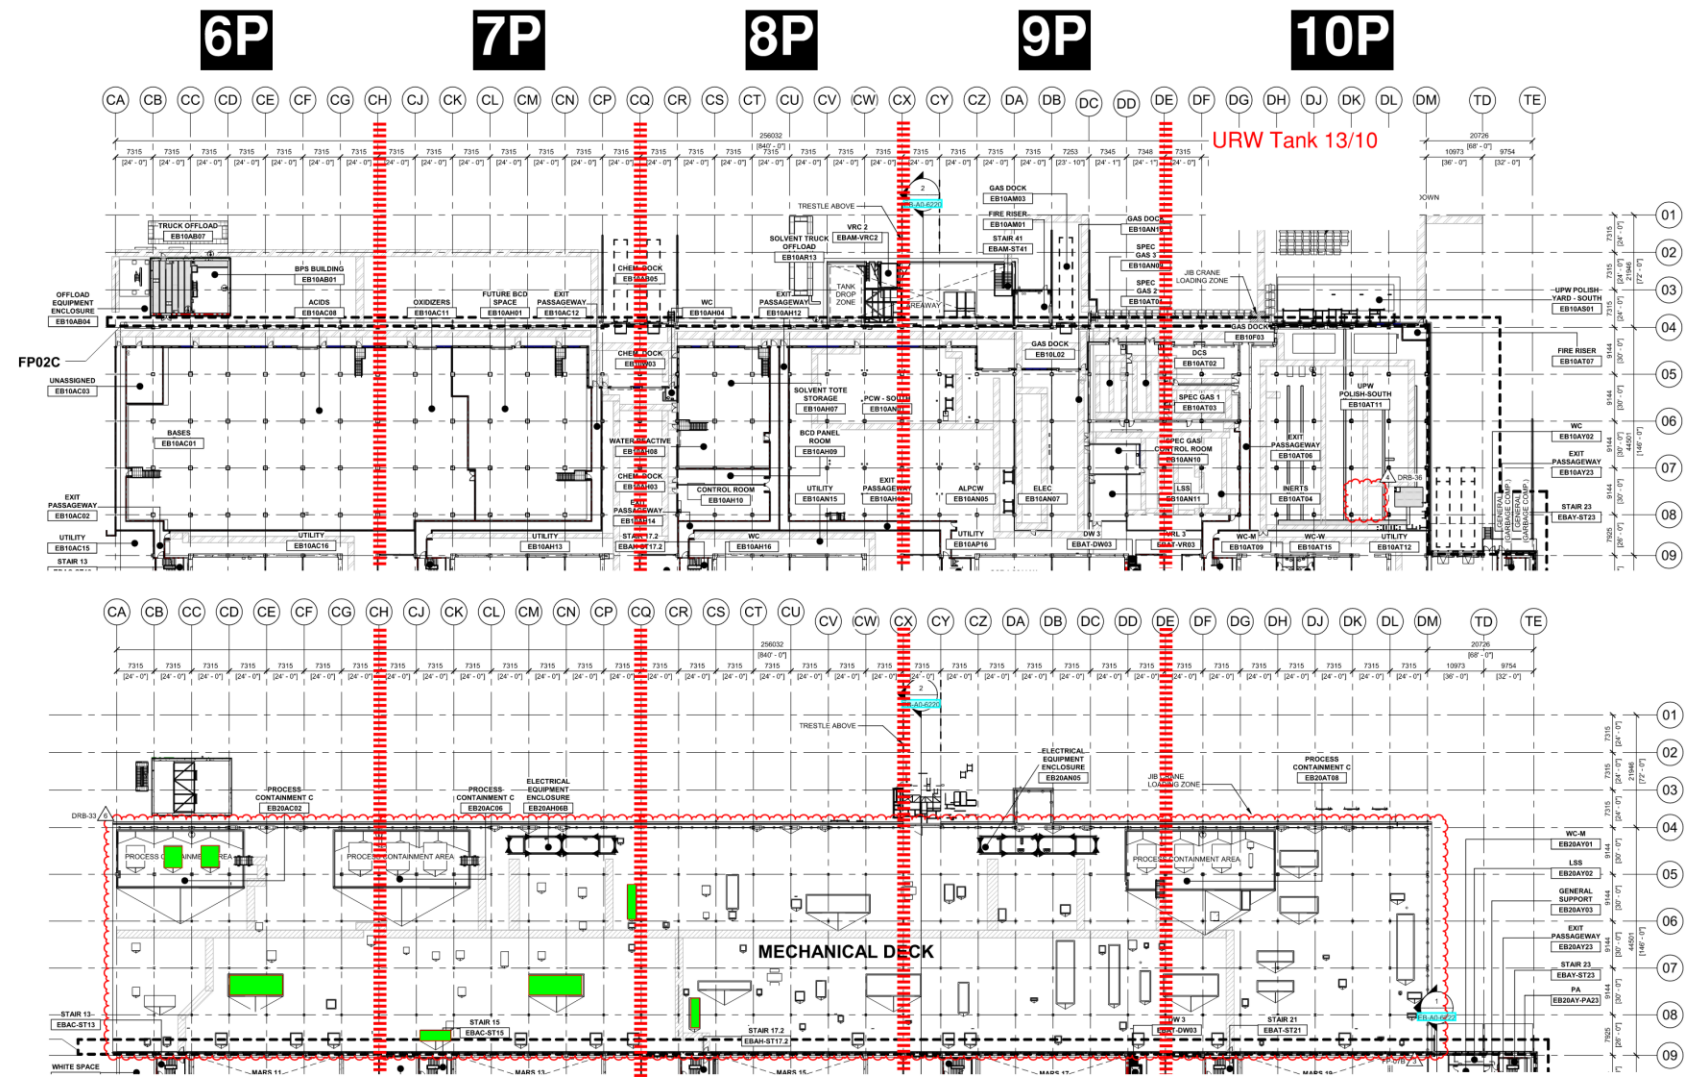



WJG 01J, 02J LIFT 2 & 3






WJG 03J, 04J, 05J LIFT 2 & 3







WJG UTILITY LEVEL BUILD OUT

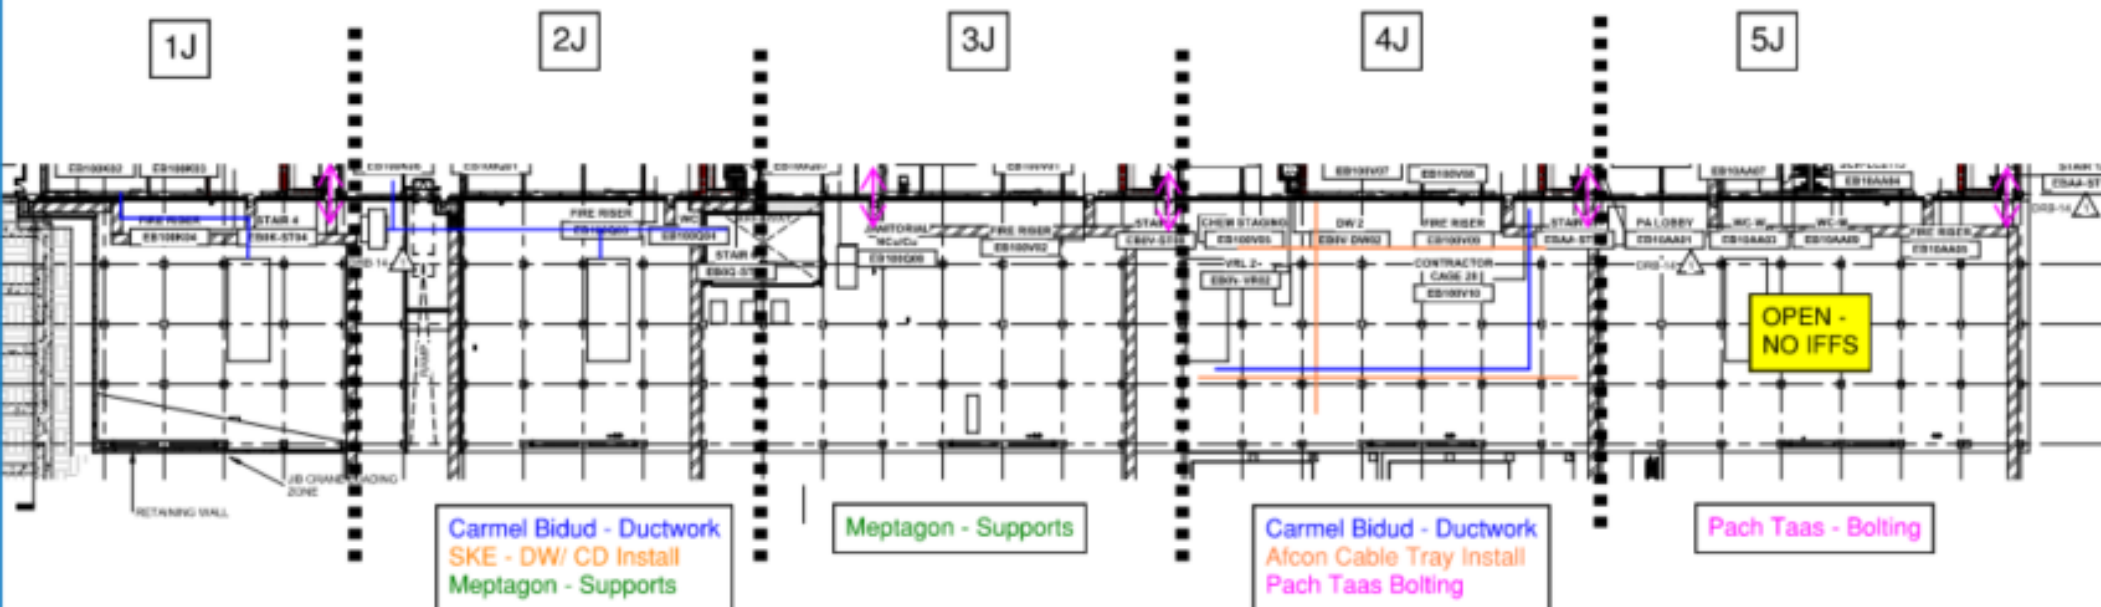

TC4 Dismantle Exclusion Zones

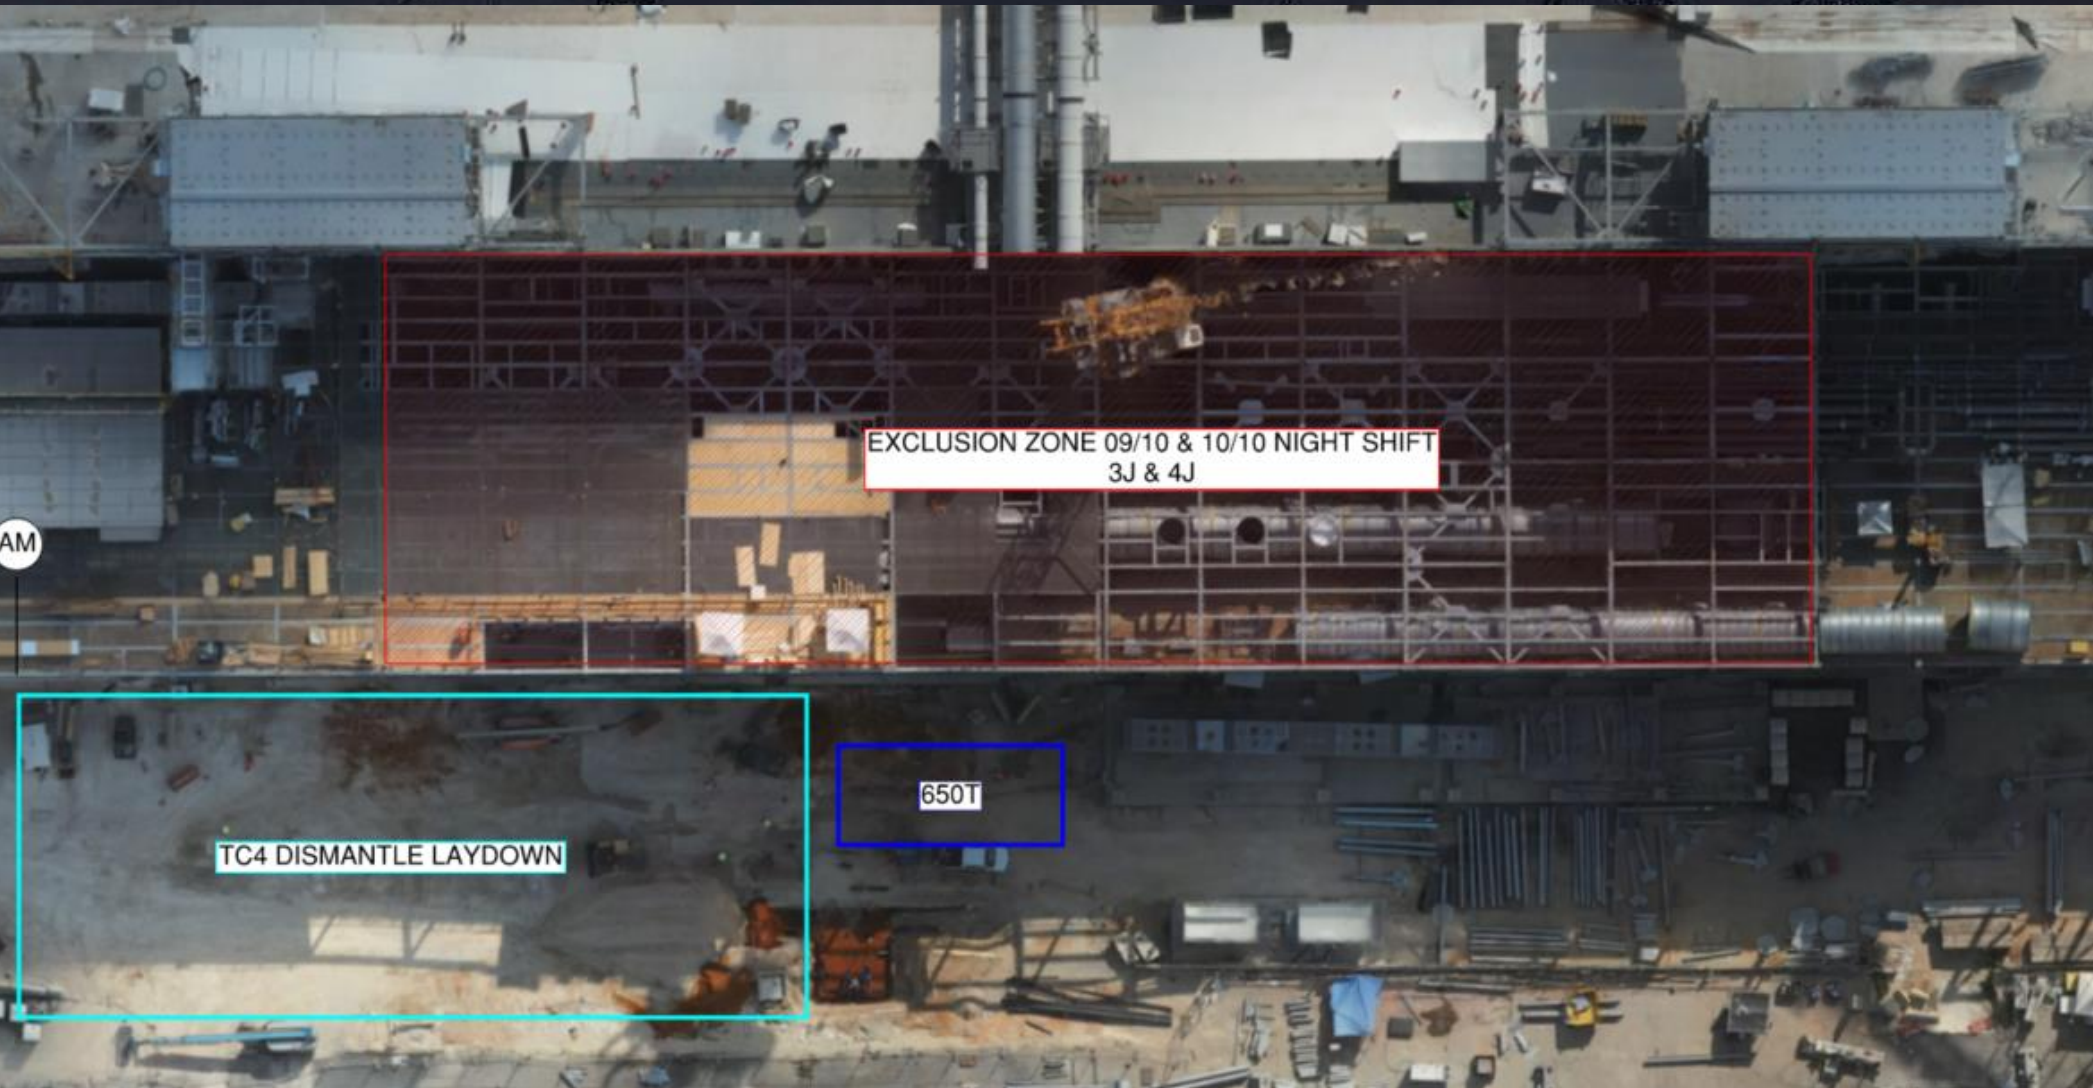

TC4 Dismantle Logistics

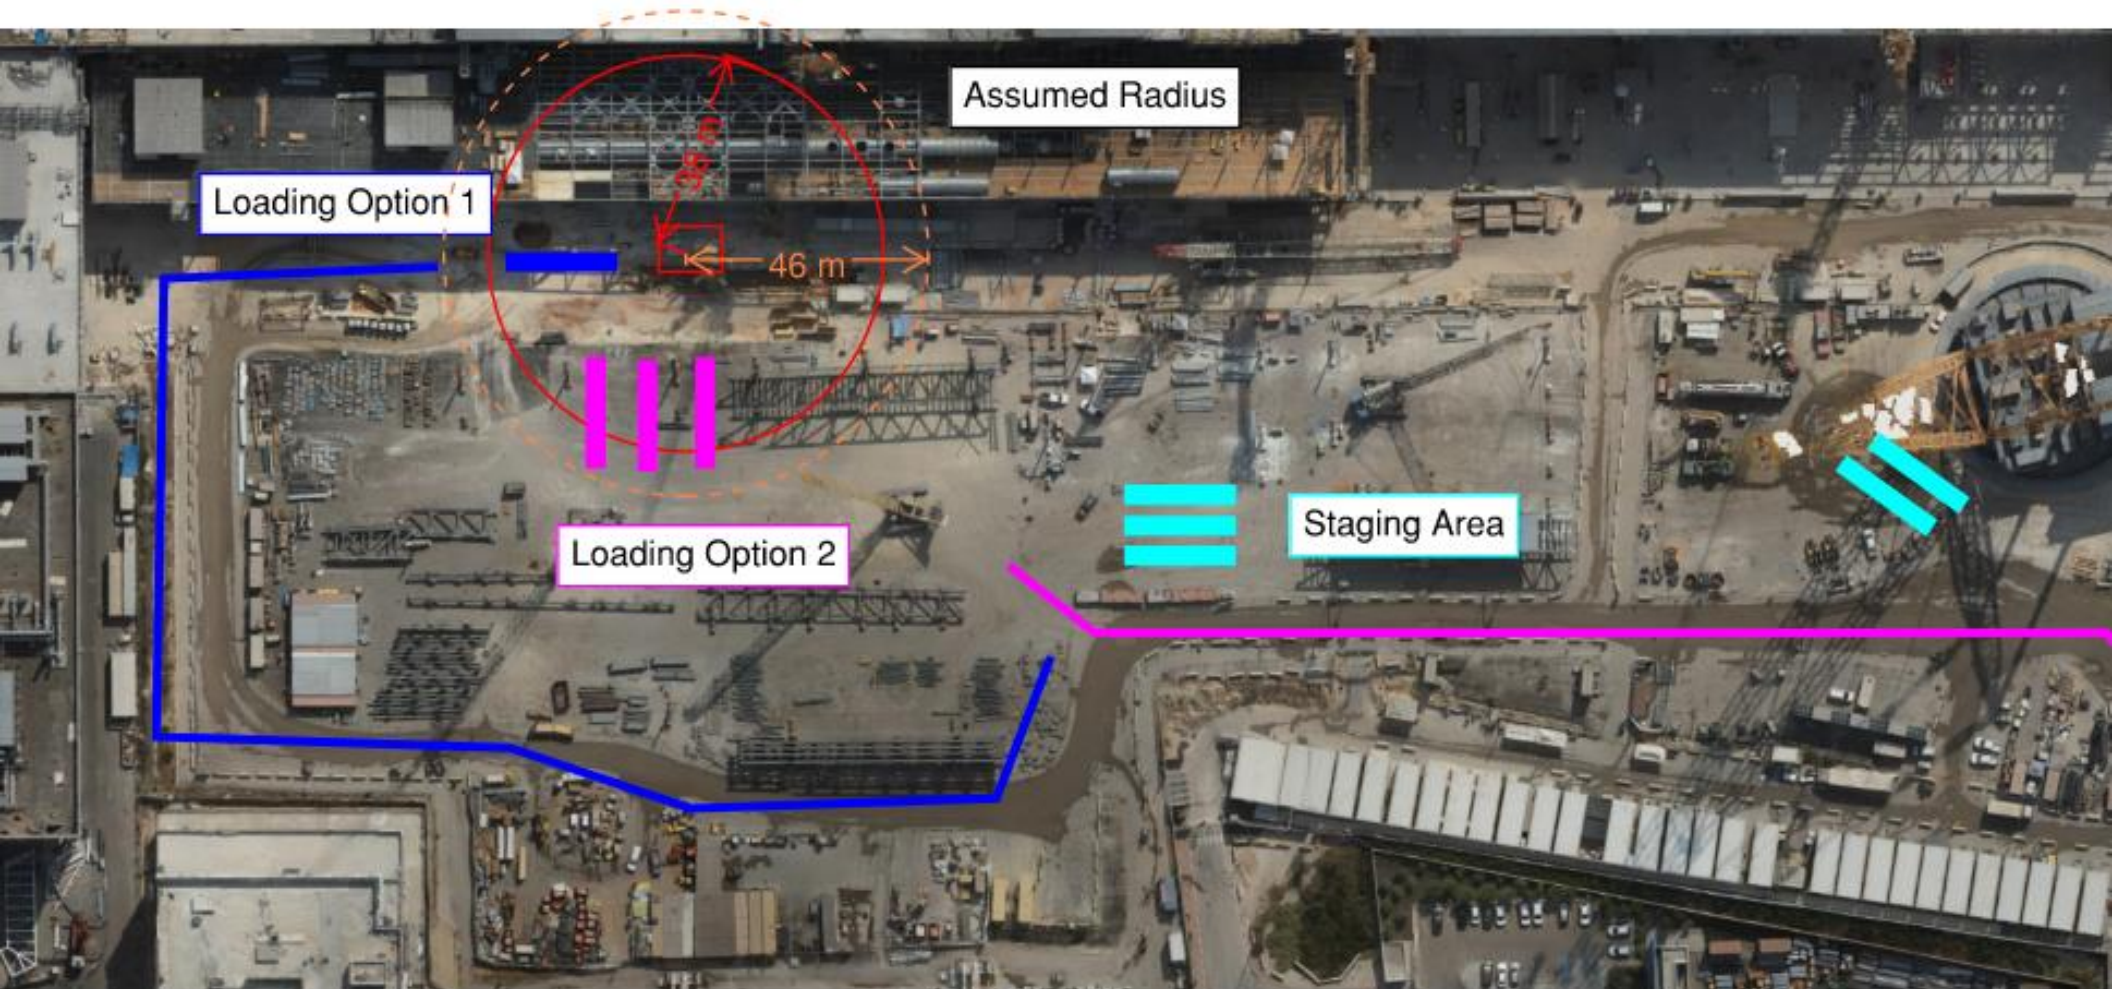

Truck Staging:

Dependent on Box Build and W&W Permission - Park Empty Trucks in Truss Yard. Other Options: In Sarens Area, or Outside Gate A (limit 2)

Truck Routing:


Option 1: Trailer north of crane, limit 1 truck only

Option 2: (Pending Box Build and W&W Permission) Stage 1-3 Trucks within 46m Radius


CUB 1

CUB 1 COORDINATION MAP

UPDATED __ / __ / __

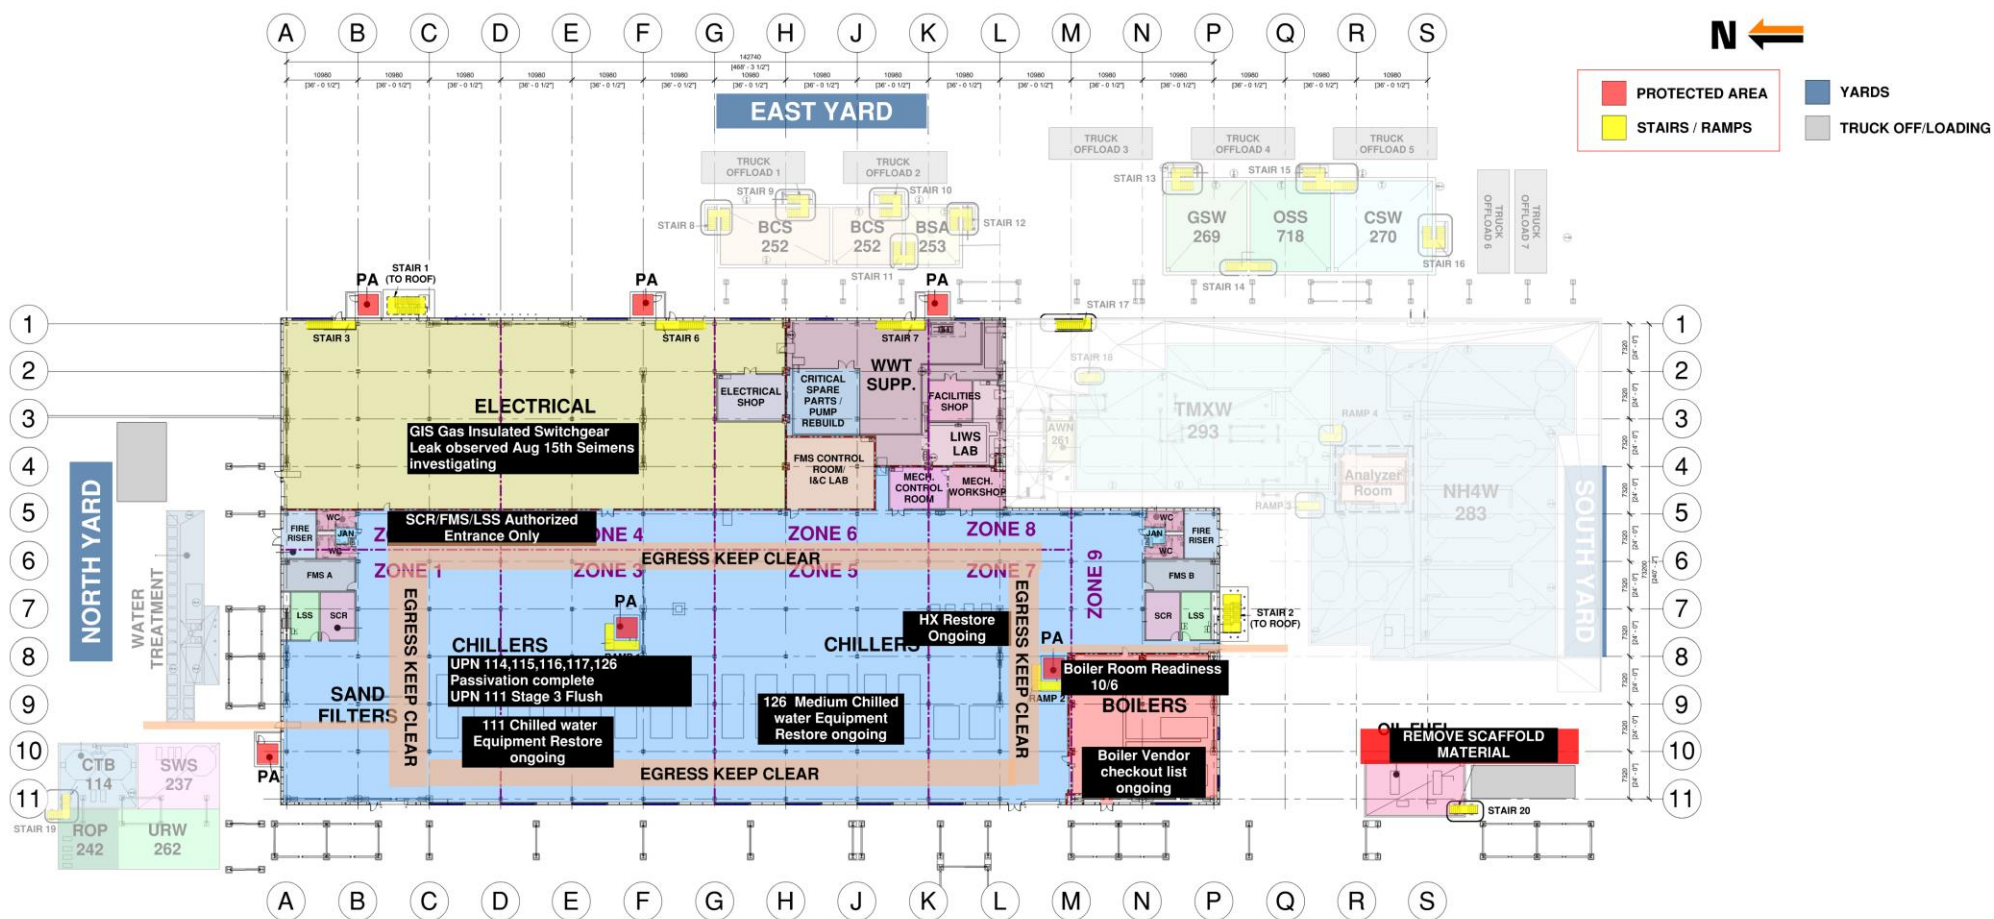

CUB 1 – EXTERIOR/ROOF

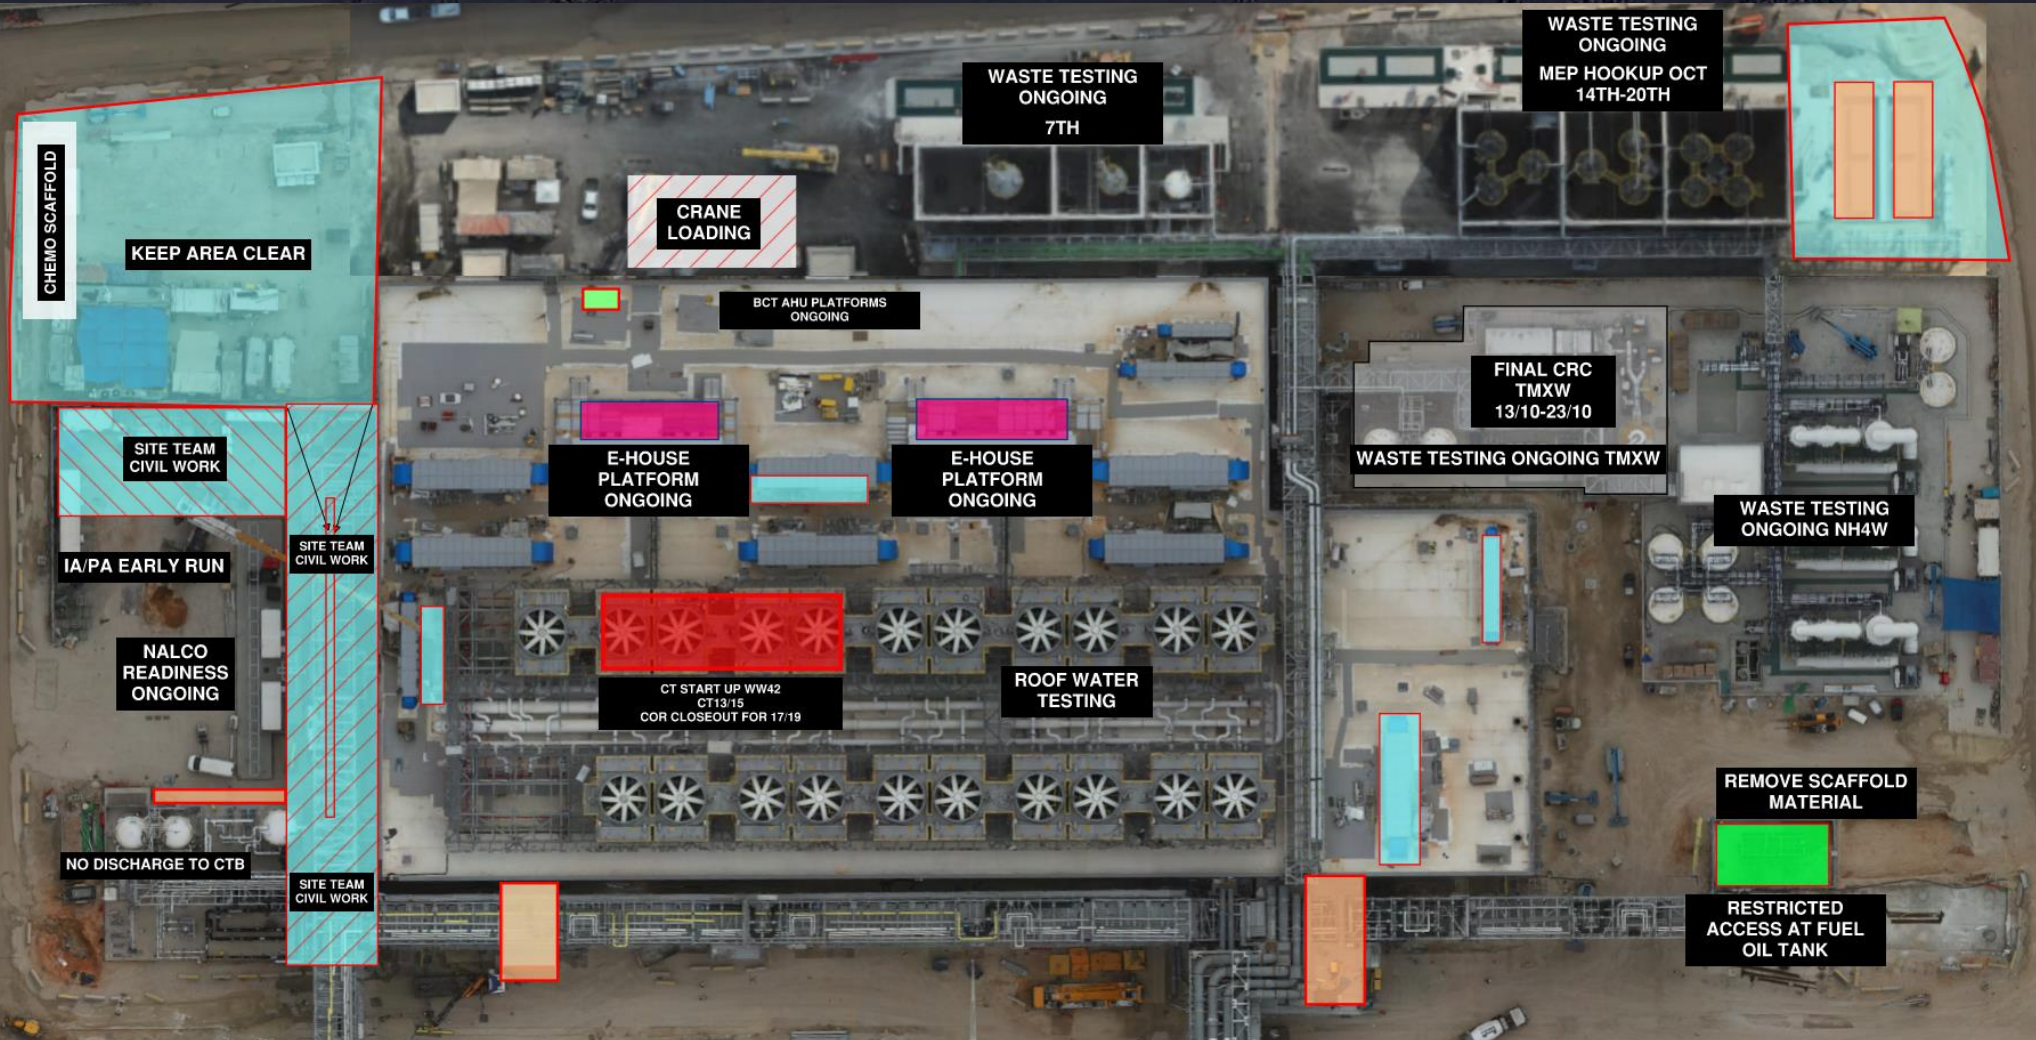




CUB 2


CUB 2 COORDINATION MAP



- PROTECTED AREA
- STAIRS / RAMPS
- YARDS
- TRUCK OFF/LOADING
- Wall Framing
- Metal Panels

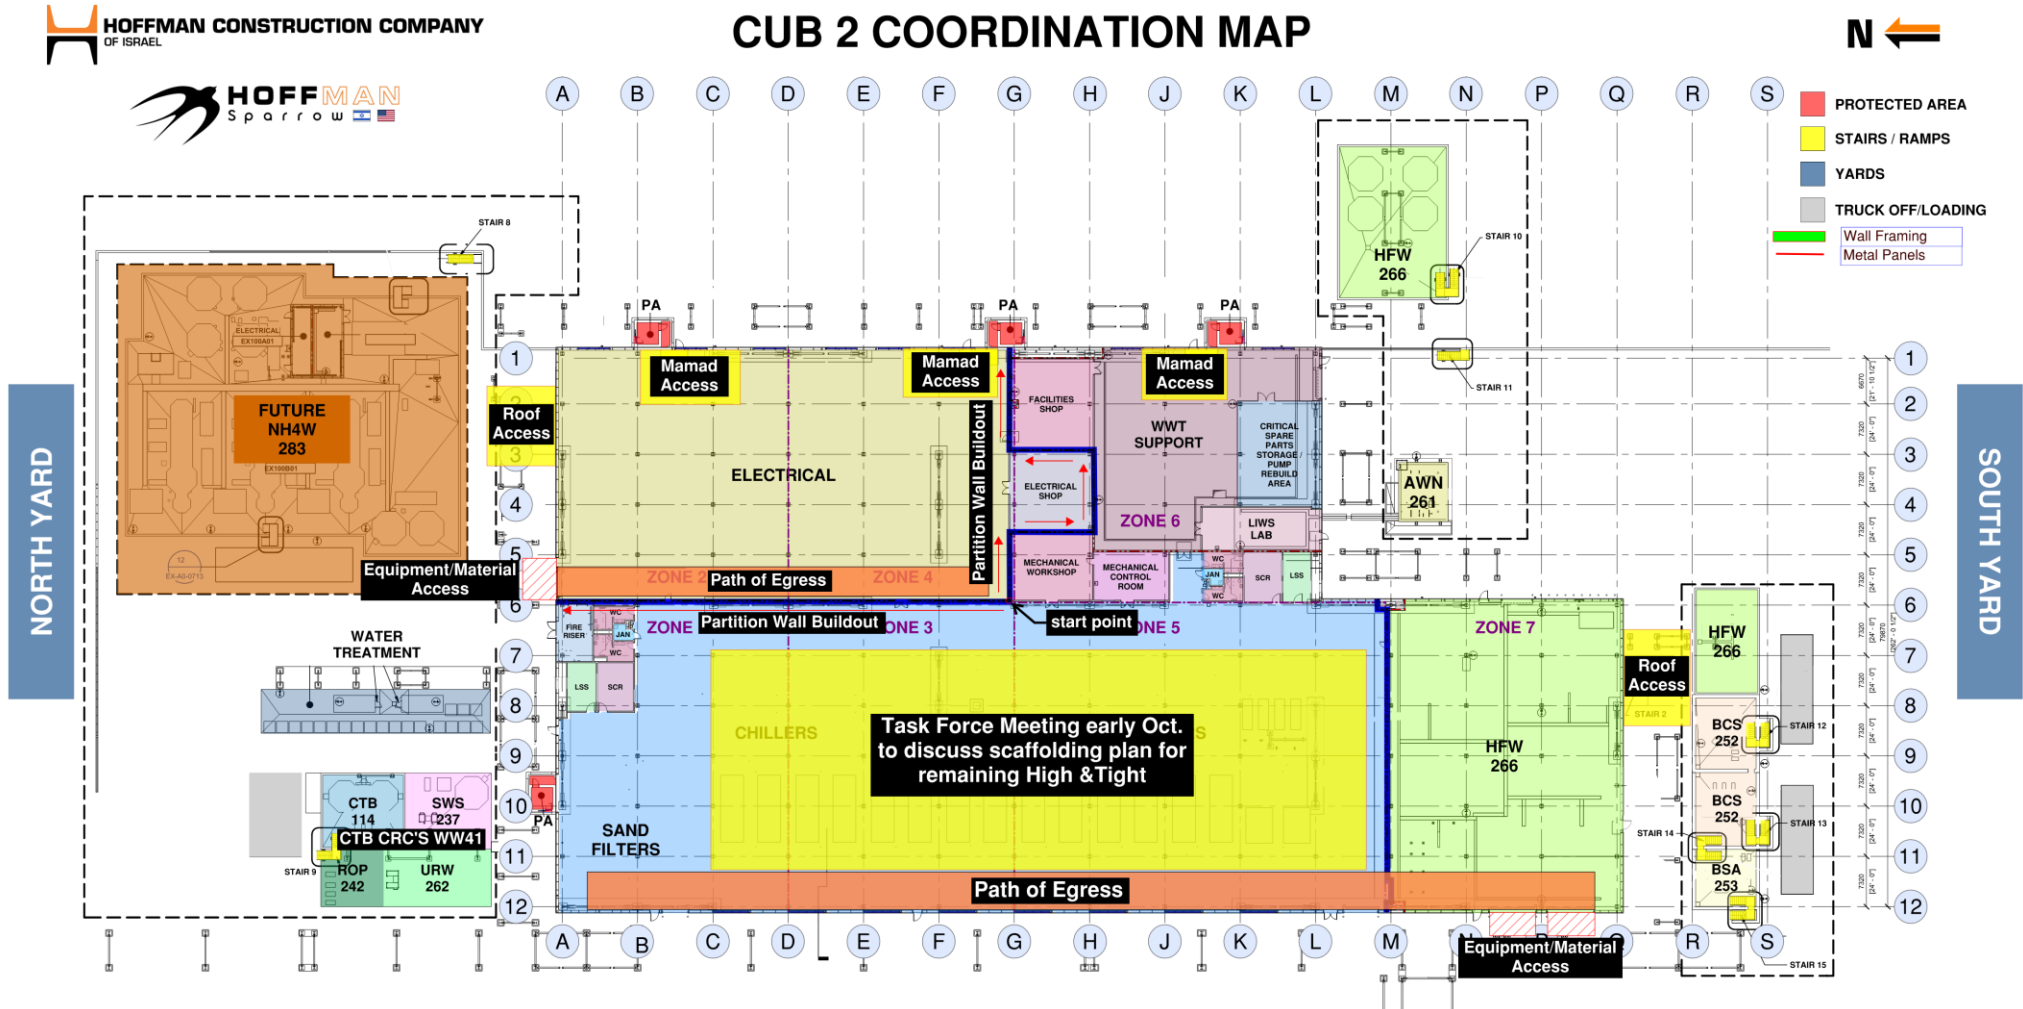

CUB 2 – EXTERIOR/ROOF

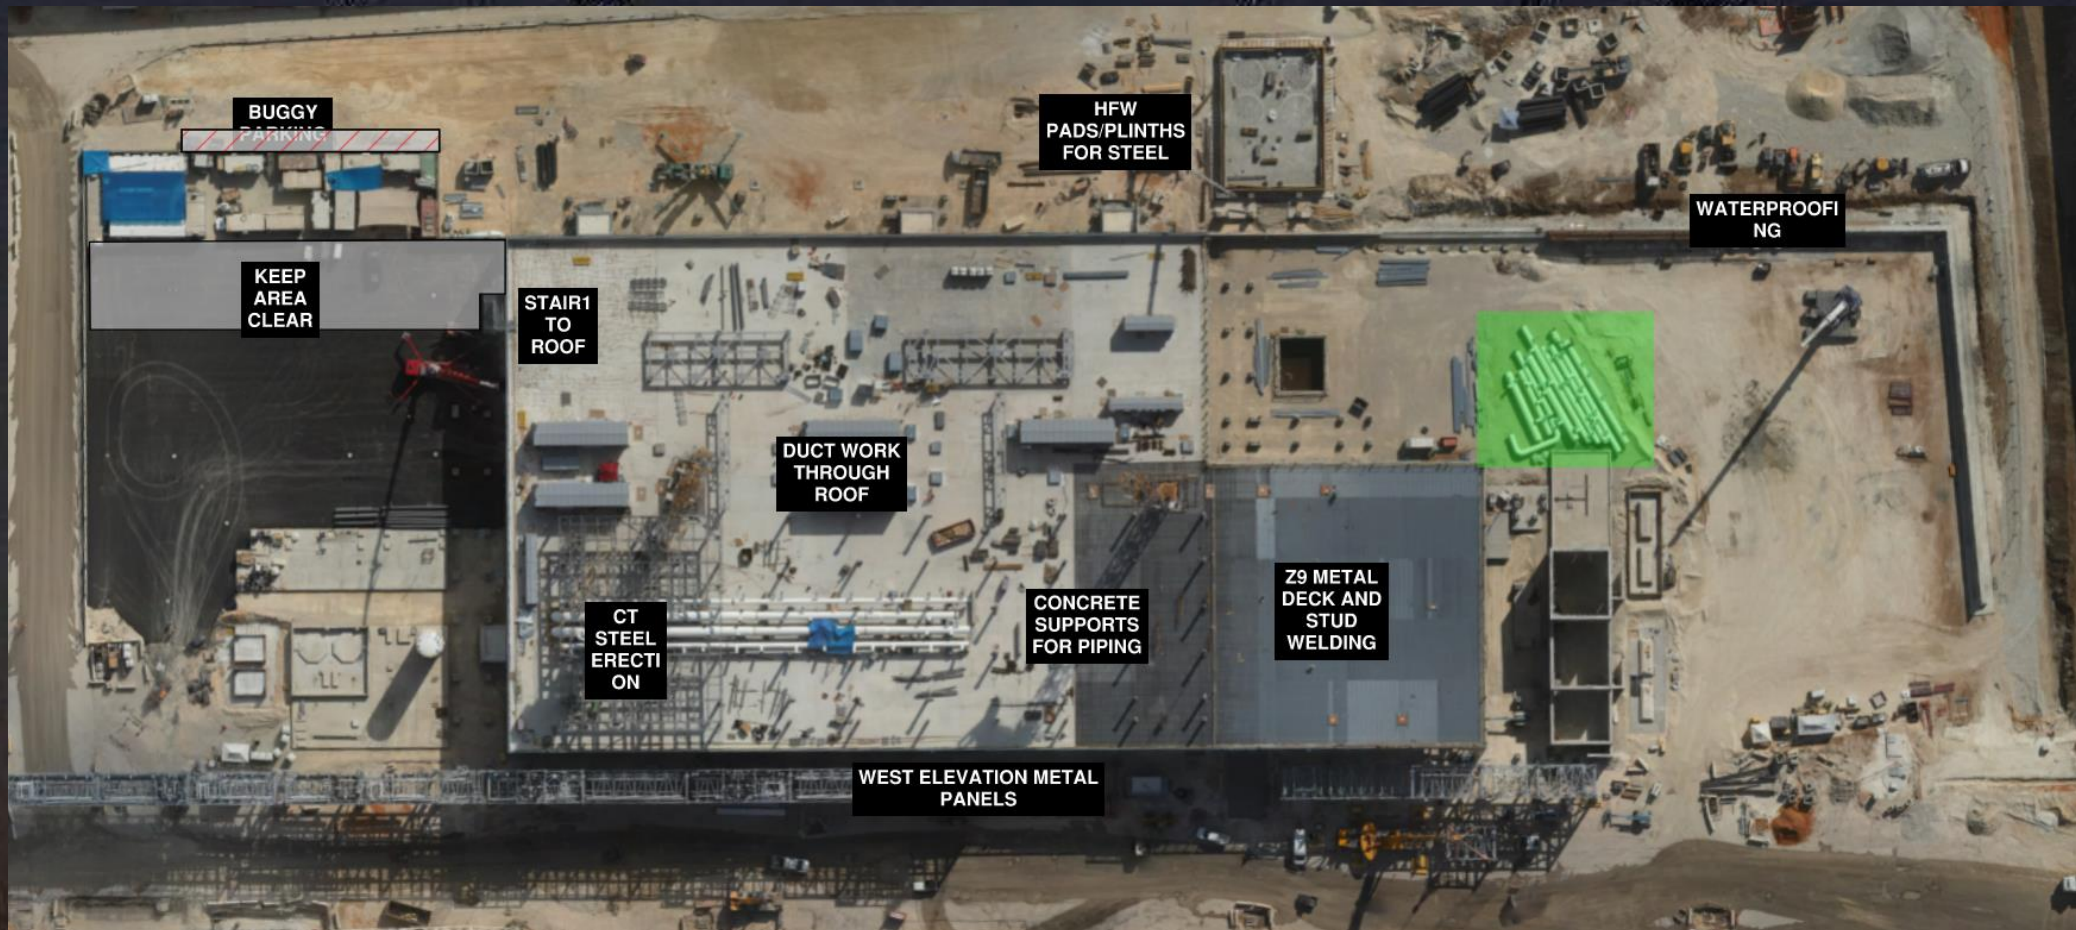



T19 -ERECTION SEQUENCE

10/OCT

06/OCT

30/sep


29/sept

25-26/sept

23-24/sept

22/sep



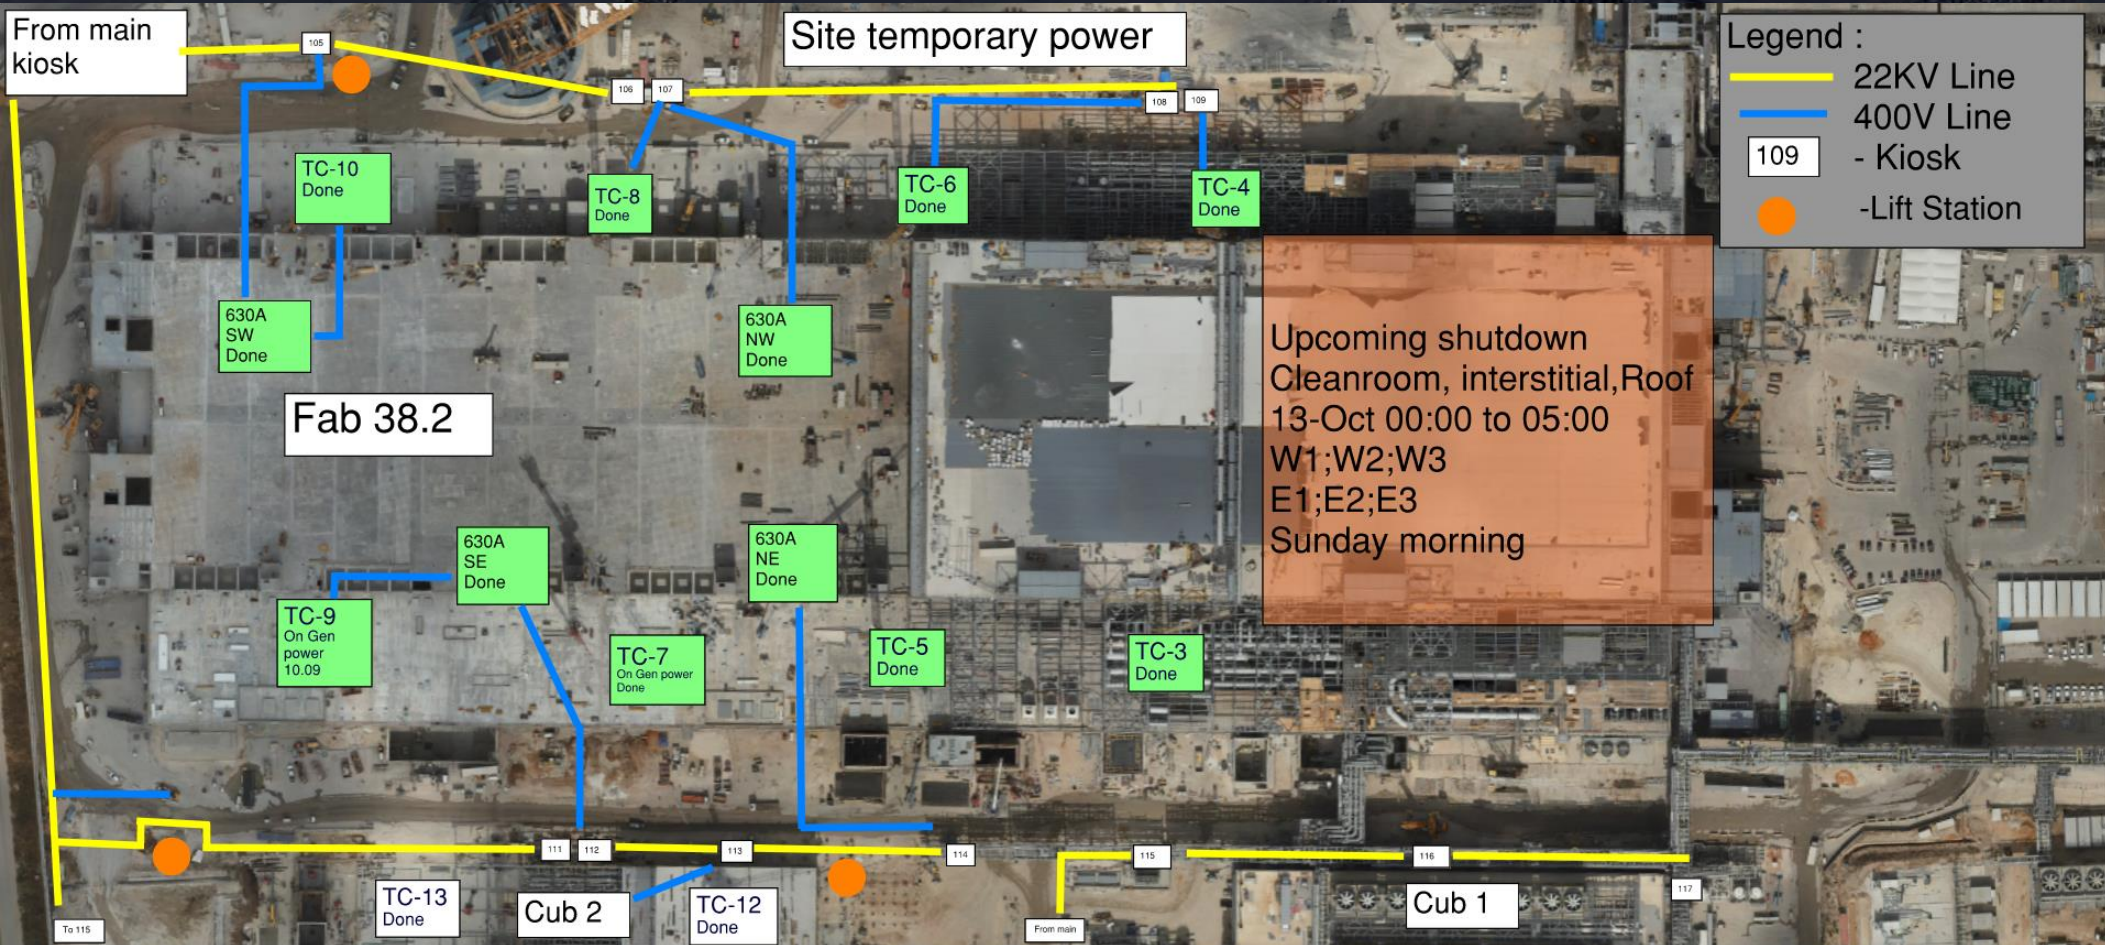

Daily Coordination Meeting

Site Logistics


North



Daily Coordination Meeting

Site Logistics

South

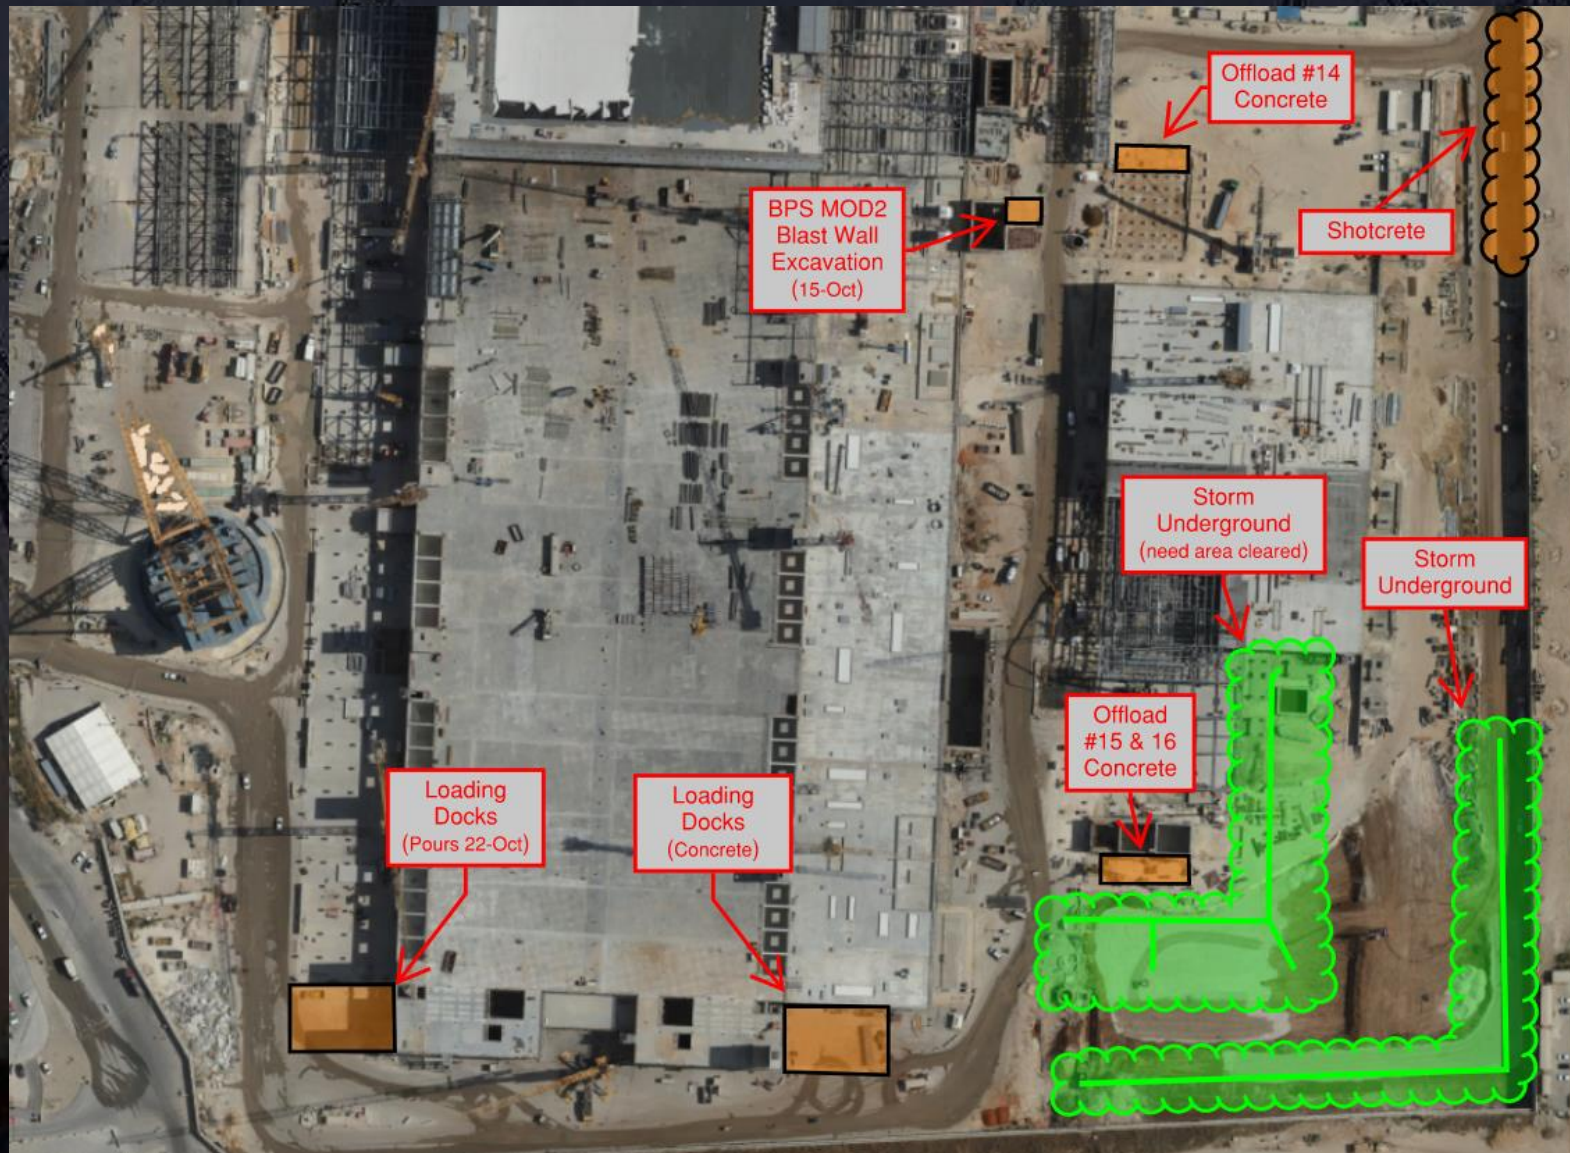





Daily Coordination Meeting

Site Logistics - Protected Areas (SUT Level)

SUT1

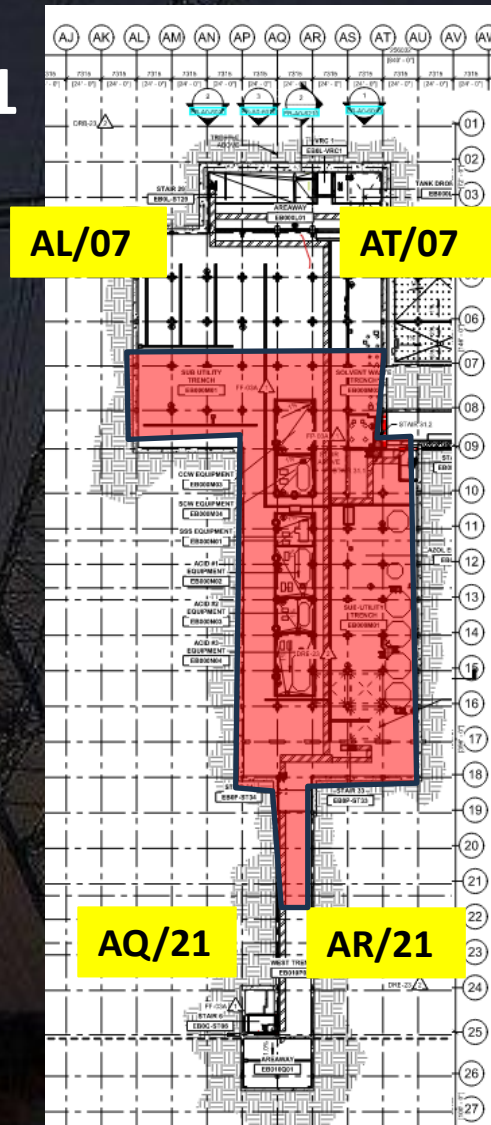


SUT2

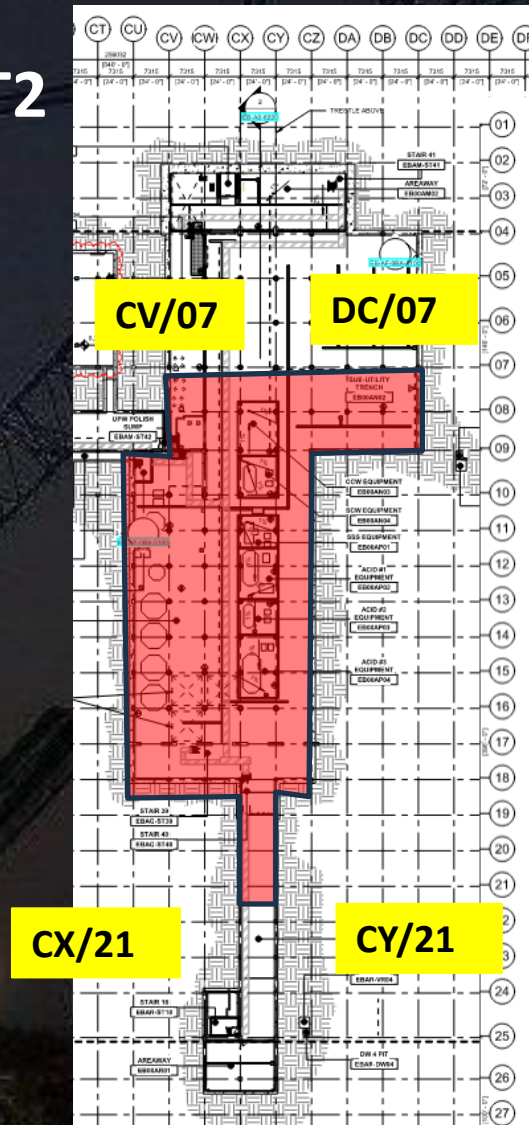

Daily Coordination Meeting


Site Logistics - Protected Areas (Utility Level)

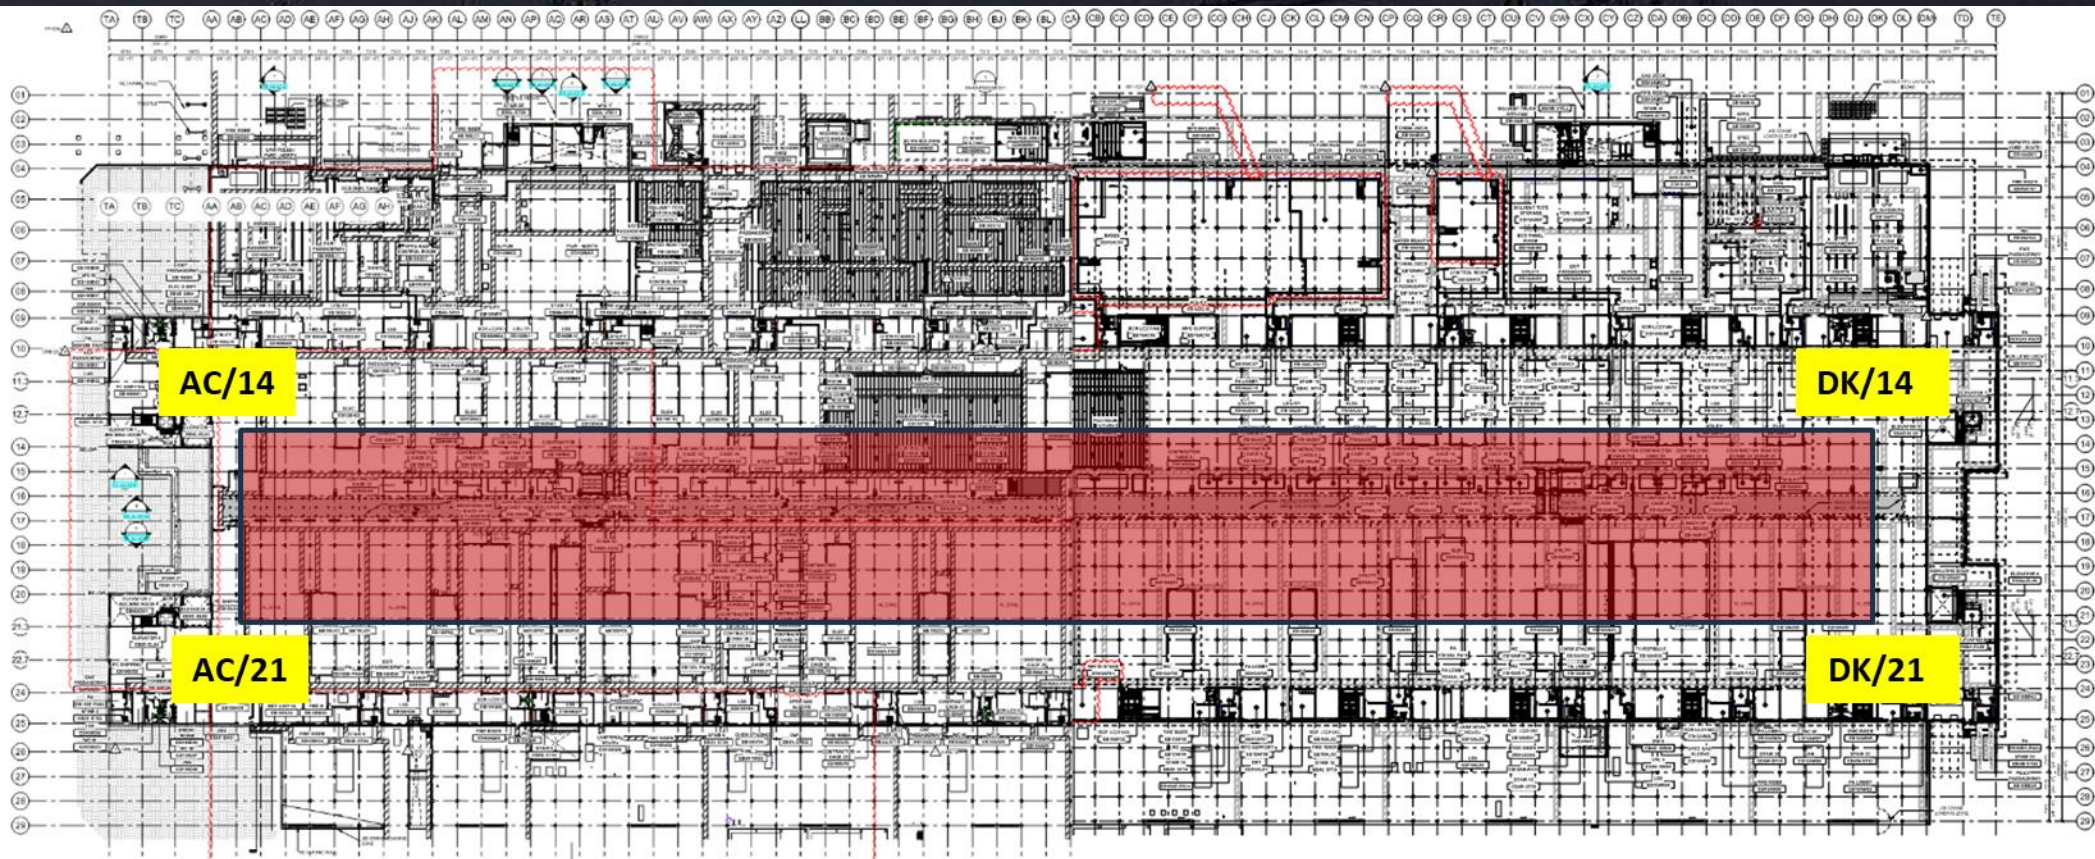



Daily Coordination Meeting


Site Logistics - Protected Areas (Subfab Level)

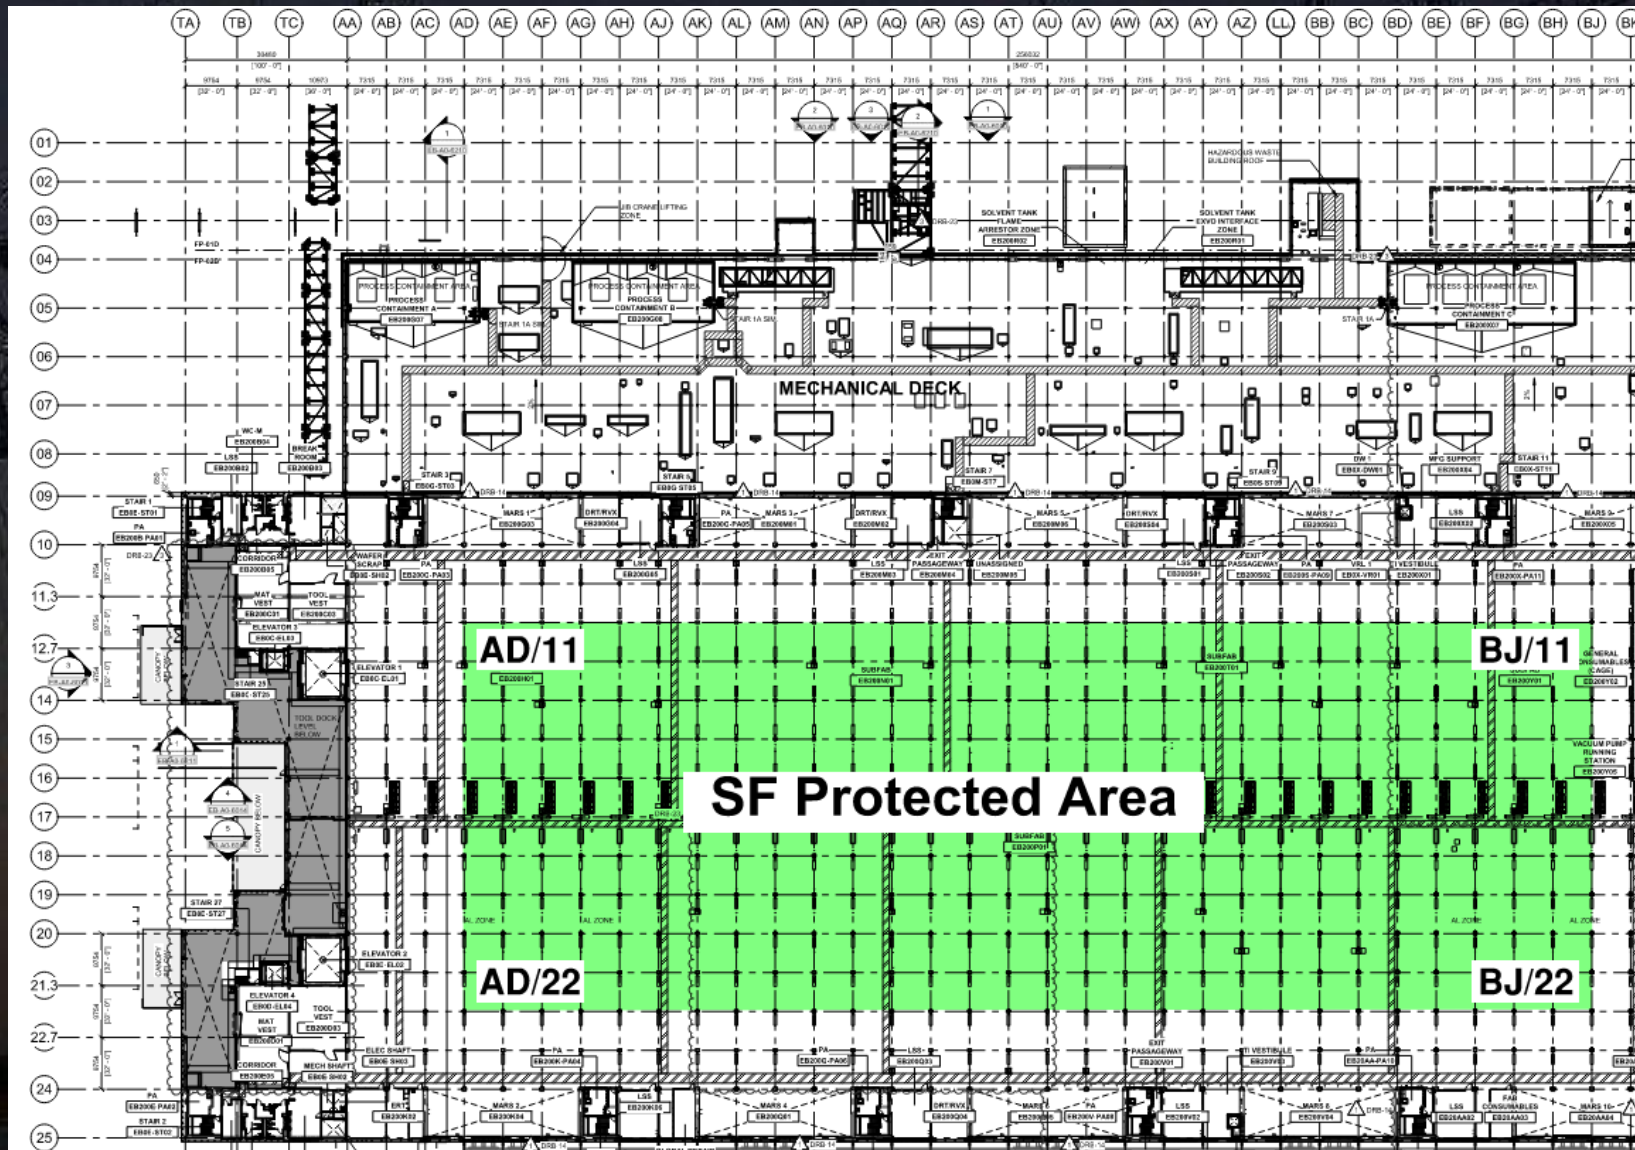

Daily Coordination Meeting

Site Logistics

Protected Areas

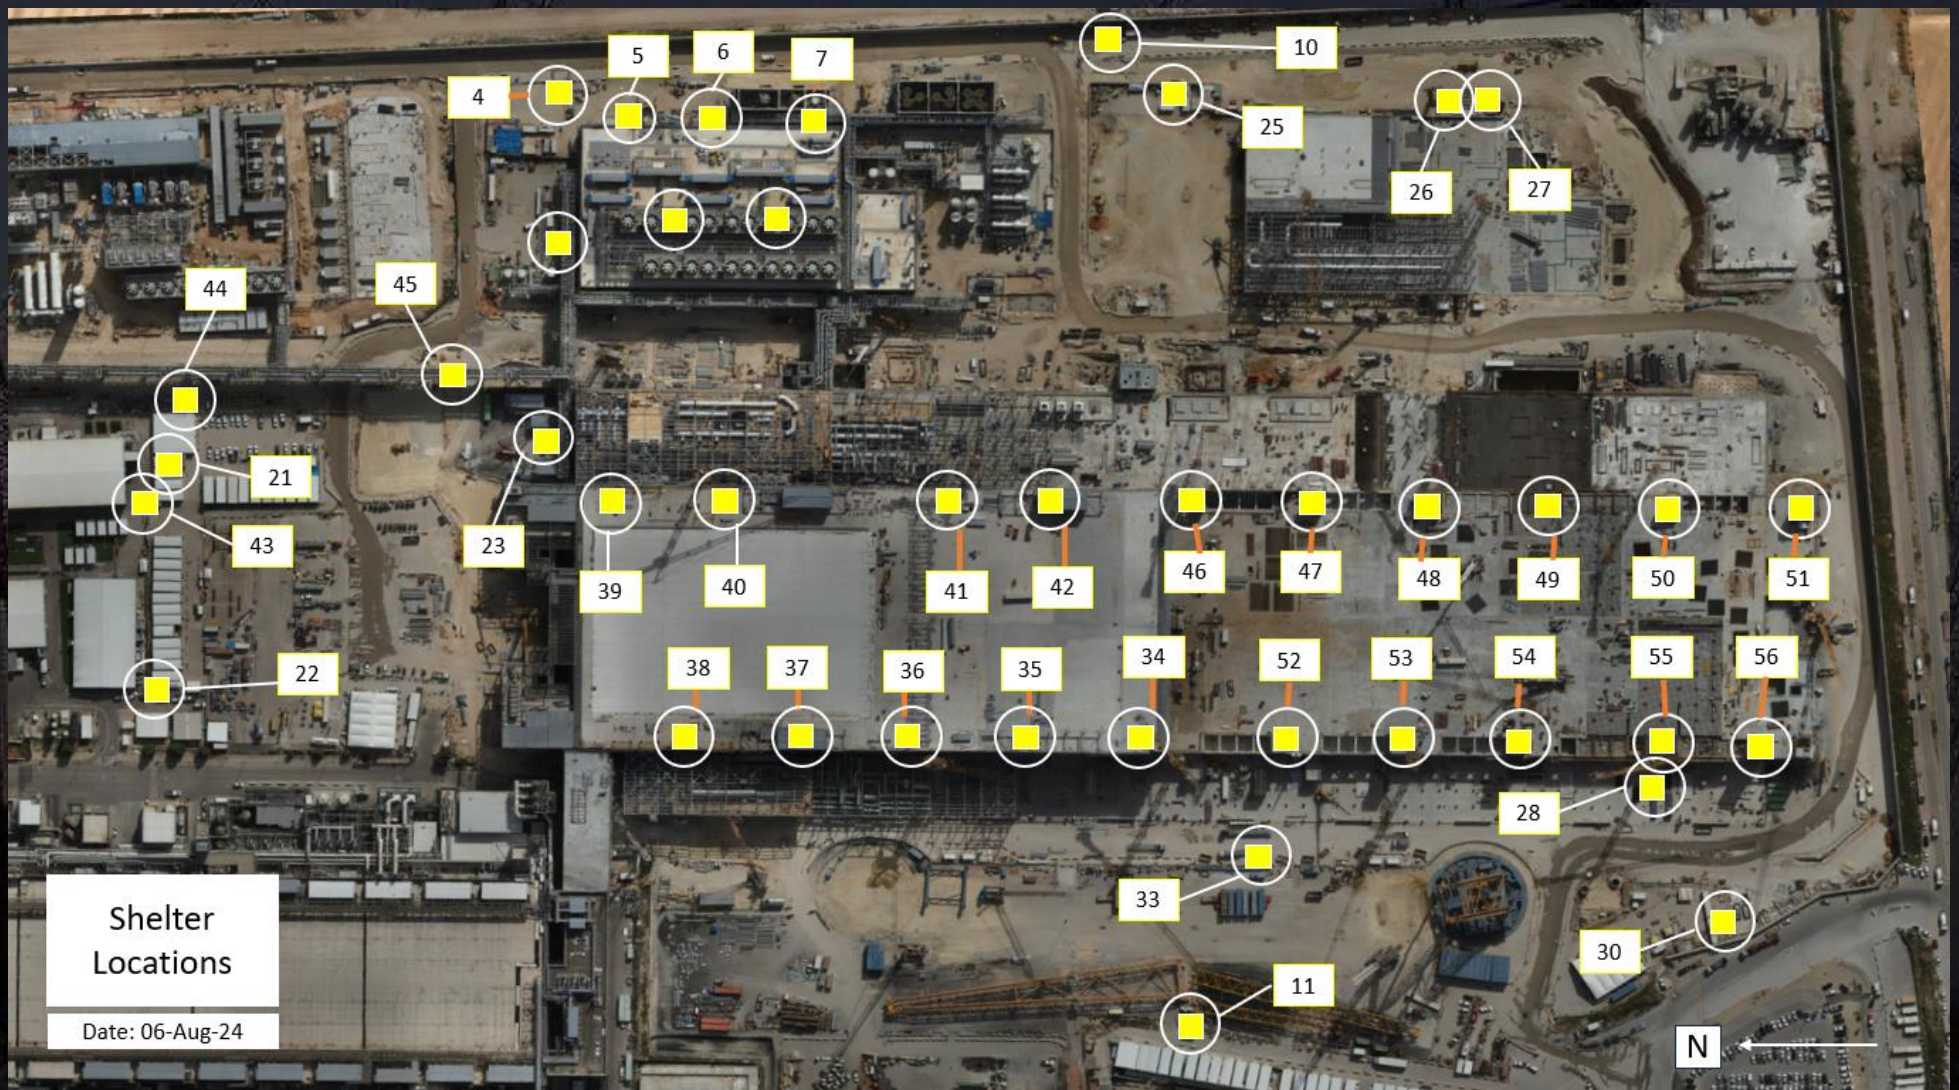



LEARN FROM EVERYTHING

PROJECT
EAGLE
2024

ALL INJURIES ARE PREVENTABLE | PEOPLE ARE THE SOLUTION | SUCCESS IS THE PRESENCE OF SAFETY

WHAT HAPPENED?

Employee was reaching for a drill on the bottom of a cart. Employee pushed the Port-a-band saw with both hands, which was hanging on the edge of the cart. When they pushed the port-a-band saw it activated and caught the employee's glove resulting in a laceration to their finger.

WHAT CORRECTIVE ACTIONS ARE BEING TAKEN?

- Contractor to update PTP to reflect hazards of energized tools when not in use.
- Purchase power tools with multiple safety devices (auto engaging safety guards).
- Toolbox Talk for tool usage (hand placement).

WHAT CAN THE PROJECT LEARN FROM THIS INCIDENT?

- Always store tools in a "safe state" (safety on, unplugged or battery removed).
- Keep hands away from tool blades.
- When purchasing power tools, try to acquire tools with multiple safety devices (auto engaging safety's, guards).





LEARN FROM EVERYTHING

ALL INJURIES ARE PREVENTABLE | PEOPLE ARE THE SOLUTION | SUCCESS IS THE PRESENCE OF SAFETY

PROJECT
EAGLE
2024



WHAT HAPPENED?

Crew was starting up transformer TNZ682, when an arch flash occurred due to a foreign loose bolt inside transformer.

WHAT CORRECTIVE ACTIONS ARE BEING TAKEN?

- Developed a “Team of 3” checklist to ensure inspection of transformer for the following categories: cleanliness, tampering, lose or foreign components, damage, fastening of bolts, safeguards, wiring components, and phase to phase processes.
- Lotus to incorporate the use of cameras, to help with pre-energization inspection.
- Install tamper tape when transformer is released.
- Conduct a toolbox talk to all contractor employees.

WHAT CAN THE PROJECT LEARN FROM THIS INCIDENT?

- Emphasize the critical importance of ensuring the cleanliness of electrical equipment. The presence of foreign objects—such as tools, debris, or other foreign objects — can lead to significant hazards and operational failures.
- Quality checks are not just for quality, there are often safety implications for systems and equipment not being installed properly or checked prior to energization. Do not “pencil whip” your QA documents.



Daily Coordination Meeting



14:00 Sign In
